




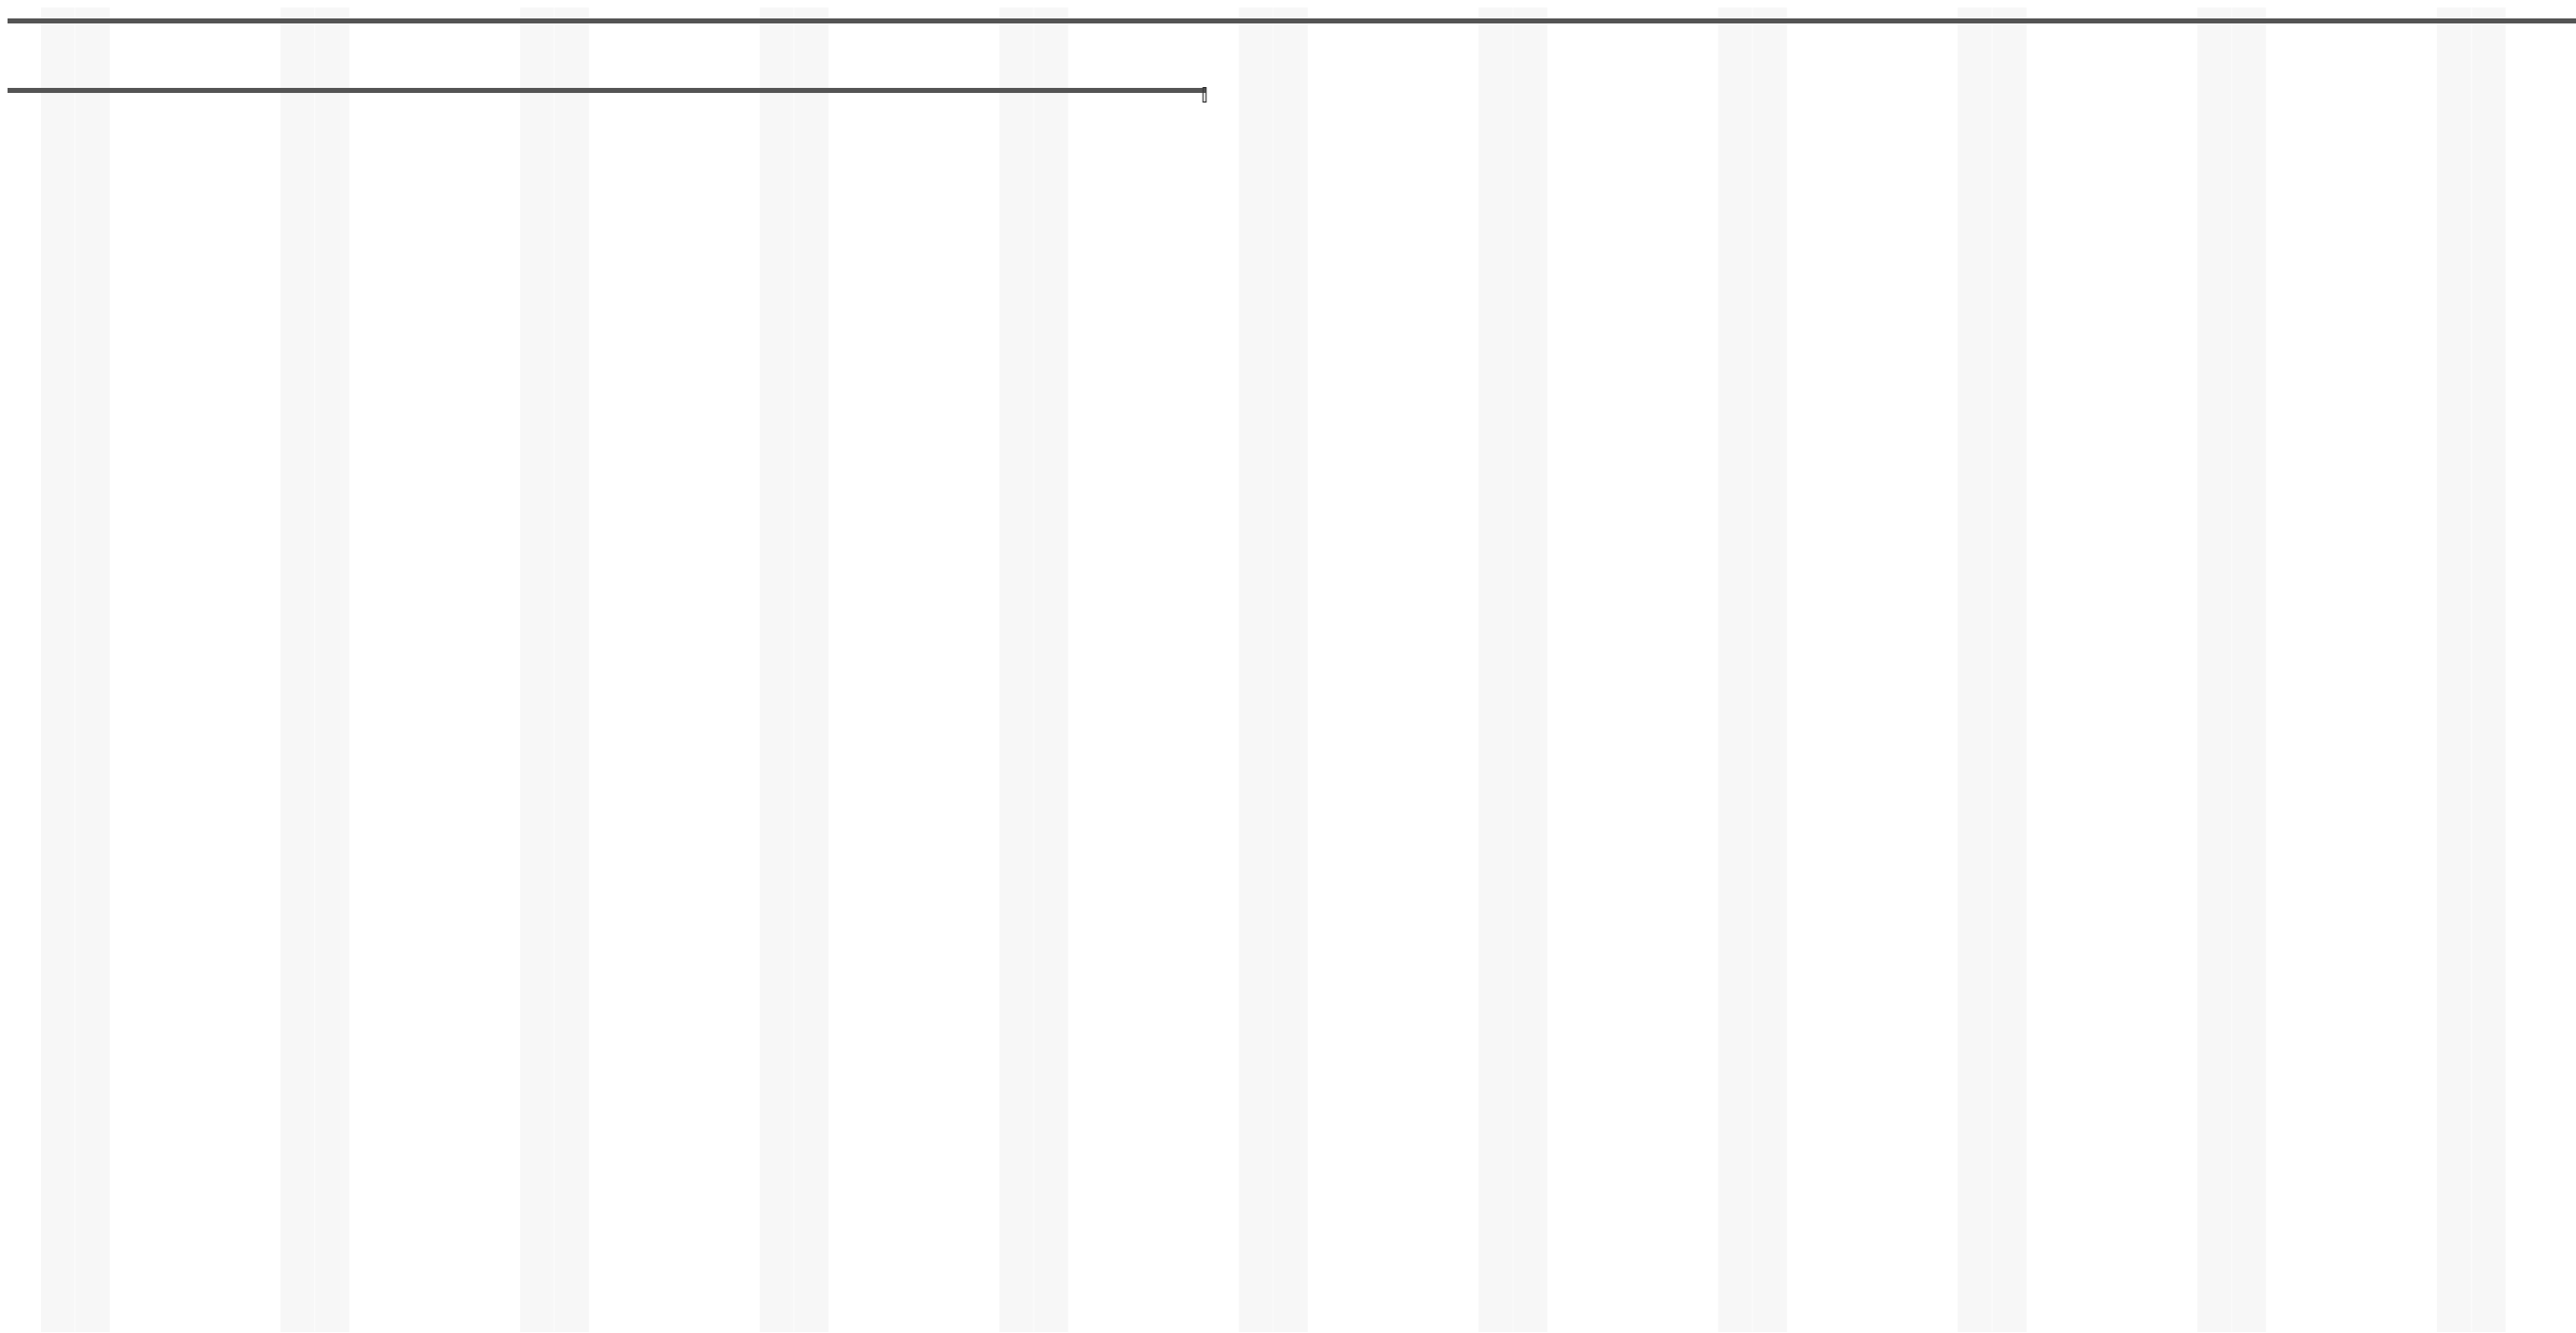
ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors
1	→	1	Cadence Bank Parking garage	340.5 days	Tue 3/2/21	Tue 6/21/22	
2	→	1.1	Project awarded	1 day	Tue 3/2/21	Tue 3/2/21	
3	→	1.2	Preconstruction (Division 000000)	48 days	Tue 3/2/21	Thu 5/6/21	
4	→	1.2.1	Contract agreement	2 days	Tue 3/2/21	Wed 3/3/21	
5	→	1.2.2	Contract plan flip	3 days	Tue 3/2/21	Thu 3/4/21	
6	→	1.2.3	Shop Drawings reinforcing steel	10 days	Thu 3/4/21	Wed 3/17/21	4
7	→	1.2.4	Shop Drawing precast panel	18 days	Tue 3/2/21	Thu 3/25/21	
8	→	1.2.5	Shop Drawing elevators	6 days	Tue 3/2/21	Tue 3/9/21	
9	→	1.2.6	Shop drawing for site utilities	7 days	Tue 3/2/21	Wed 3/10/21	
10	→	1.2.7	Shop drawing review	10 days	Thu 3/18/21	Wed 3/31/21	6
11	→	1.2.8	Building drawings	35 days	Tue 3/2/21	Mon 4/19/21	
12	→	1.2.9	Building permit	13 days	Tue 4/20/21	Thu 5/6/21	11
13	→	1.2.10	Meet about budget	2 days	Tue 3/2/21	Wed 3/3/21	
14	→	1.2.11	Signed insurance documents	1 day	Tue 3/2/21	Tue 3/2/21	
15	→		Go over safety plan	2 days	Tue 3/2/21		
18	→	1.2.15	Permit approved	1 day	Tue 4/20/21	Tue 4/20/21	11
19	→	1.2.16	Subcontractor bid	1 day	Wed 4/21/21	Wed 4/21/21	17
20	→	1.2.17	Subcontractor award date	30 days	Tue 3/2/21	Mon 4/12/21	
21	→	1.3	Sitework (Division 010000)	1 day	Tue 4/13/21	Tue 4/13/21	19
22	→	1.3.1	Mobilize job trailer	42.25 days	Wed 4/14/21	Fri 6/11/21	
23	→	1.3.2	Insert jobsite fence	16 days	Wed 4/14/21	Wed 5/5/21	20
24	→	1.3.3	Put up jobsite signs	1 day	Thu 5/6/21	Thu 5/6/21	22
				0.5 days	Fri 5/7/21	Fri 5/7/21	23

ID	 Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors
39		1.3.18					







ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors
77	→	1.6.8	Place horizontal beams span 2 floor P3	2 days	Mon 8/30/21	Tue 8/31/21	76
78	→	1.6.9	Place horizontal beams span 3 floor P3	2 days	Wed 9/1/21	Thu 9/2/21	77
79	→	1.6.10	Set span 1 double Ts P1	4 days	Fri 9/3/21	Wed 9/8/21	78
80	→	1.6.11	Insert temporary railing	1 day	Thu 9/9/21	Thu 9/9/21	79
81	→	1.6.12	Set span 2 double Ts P1	4 days	Fri 9/10/21	Wed 9/15/21	80
82	→	1.6.13	Insert temporary railing	1 day	Thu 9/16/21	Thu 9/16/21	81
83	→	1.6.14	Set span 3 double Ts P1	4 days	Fri 9/17/21	Wed 9/22/21	82
84	→	1.6.15	Insert temporary railing	1 day	Thu 9/23/21	Thu 9/23/21	83
85	→	1.6.16	Set span 1 double Ts P2	4 days	Fri 9/24/21	Wed 9/29/21	84
86	→	1.6.17	Insert temporary railing	1 day	Thu 9/30/21	Thu 9/30/21	85
87	→	1.6.18	Set span span 2 double Ts P2	4 days	Fri 10/1/21	Wed 10/6/21	86
88	→	1.6.19	Insert temporary railing	1 day	Thu 10/7/21	Thu 10/7/21	87
89	→	1.6.20	Set span 3 double Ts P2	4 days	Fri 10/8/21	Wed 10/13/21	88
90	→	1.6.21	Insert temporary railing	1 day	Thu 10/14/21	Thu 10/14/21	89
91	→	1.6.22	Set span 1 double Ts P3	4 days	Fri 10/15/21	Wed 10/20/21	90
92	→	1.6.23	Insert temporary railing	1 day	Thu 10/21/21	Thu 10/21/21	91
93	→	1.6.24	Set span 2 double Ts P3	4 days	Fri 10/22/21	Wed 10/27/21	92
94	→	1.6.25	Insert temporary railing	1 day	Thu 10/28/21	Thu 10/28/21	93
95	→	1.6.26	Set span 3 double Ts P3	4 days	Fri 10/29/21	Wed 11/3/21	94
96	→	1.6.27	Insert temporary railing	1 day	Thu 11/4/21	Thu 11/4/21	95
97	→	1.6.28	Reinforce/Pour span 1 topping P1	3 days	Fri 9/10/21	Tue 9/14/21	80
98	→	1.6.29	Reinforce/Pour span 2 topping P1	3 days	Fri 9/17/21	Tue 9/21/21	82
99	→	1.6.30	Reinforce/Pour span 3 topping P1	3 days	Fri 9/24/21	Tue 9/28/21	84
100	→	1.6.31	Reinforce/Pour span 1 topping P2	3 days	Fri 10/1/21	Tue 10/5/21	86
101	→	1.6.32	Reinforce/Pour span 2 topping P2	3 days	Fri 10/8/21	Tue 10/12/21	88
102	→	1.6.33	Reinforce/Pour span 3 topping P2	3 days	Fri 10/15/21	Tue 10/19/21	90
103	→	1.6.34	Reinforce/Pour span 1 topping P3	3 days	Fri 10/22/21	Tue 10/26/21	92
104	→	1.6.35	Reinforce/Pour span 2 topping P3	3 days	Fri 10/29/21	Tue 11/2/21	94
105	→	1.6.36	Reinforce/Pour span 3 topping P3	3 days	Fri 11/5/21	Tue 11/9/21	96
106	→	1.7	Elevator/Stairs (Division 142000)	36 days	Thu 11/4/21	Thu 12/23/21	
107	→	1.7.1	Set up scaffoldings	1 day	Thu 11/4/21	Thu 11/4/21	95
108	→	1.7.2	Formwork for Elevator shaft P1	1 day	Fri 11/5/21	Fri 11/5/21	107
109	→	1.7.3	Pour shaft P1	2 days	Mon 11/8/21	Tue 11/9/21	108
110	→	1.7.4	Formwork for Elevator shaft P2	1 day	Wed 11/10/21	Wed 11/10/21	109
111	→	1.7.5	Pour shaft P2	2 days	Thu 11/11/21	Fri 11/12/21	110
112	→	1.7.6	Formwork for Elevator shaft P3	1 day	Mon 11/15/21	Mon 11/15/21	111
113	→	1.7.7	Pour shaft P3	2 days	Tue 11/16/21	Wed 11/17/21	112
114	→	1.7.8	Set up scaffolding	1 day	Thu 11/18/21	Thu 11/18/21	113


ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors
115		1.7.9	Pour stairwell pit	2 days	Fri 11/19/21	Mon 11/22/21	114
116		1.7.10	Formwork for stairwell shaft P1	1 day	Tue 11/23/21	Tue 11/23/21	115
117		1.7.11	Pour shaft P1	2 days	Wed 11/24/21	Thu 11/25/21	116
118		1.7.12	Formwork for stairwell shaft P2	1 day	Fri 11/26/21	Fri 11/26/21	117
119		1.7.13	Pour shaft P2	2 days	Mon 11/29/21	Tue 11/30/21	118
120		1.7.14	Formwork for stairwell shaft P3	1 day	Wed 12/1/21	Wed 12/1/21	119
121		1.7.15	Pour shaft P3	2 days	Thu 12/2/21	Fri 12/3/21	120
122		1.7.16	Insert and secure stair system	2 days	Mon 12/6/21	Tue 12/7/21	121
123		1.7.17	Set up scaffolding	1 day	Wed 12/8/21	Wed 12/8/21	122
124		1.7.18	Formwork for stairwell shaft P1	1 day	Thu 12/9/21	Thu 12/9/21	123
125		1.7.19	Pour shaft P1	2 days	Fri 12/10/21	Mon 12/13/21	124
126		1.7.20	Formwork for stairwell shaft P2	1 day	Tue 12/14/21	Tue 12/14/21	125
127		1.7.21	Pour shaft P2	2 days	Wed 12/15/21	Thu 12/16/21	126
128		1.7.22	Formwork for stairwell shaft P3	1 day	Fri 12/17/21	Fri 12/17/21	127
129		1.7.23	Pour shaft P3	2 days	Mon 12/20/21	Tue 12/21/21	128
130		1.7.24	Insert and secure stair system	2 days	Wed 12/22/21	Thu 12/23/21	129
131		1.8	Cladding (Division 034000)	32.5 days	Fri 12/24/21	Tue 2/8/22	
132		1.8.1	Insert and attach precast panels	26.5 days	Fri 12/24/21	Mon 1/31/22	130
133		1.8.2	Install live awning system	6 days	Mon 1/31/22	Tue 2/8/22	132
134		1.9	Mechanical/Electrical (Division 230000/260000)	89 days	Mon 1/31/22	Fri 6/3/22	
135		1.9.1	Run conduit for lights	9 days	Mon 1/31/22	Fri 2/11/22	132
136		1.9.2	Run conduit for elevator	1 day	Mon 1/31/22	Tue 2/1/22	132
137		1.9.3	Install A/C system for retail	3 days	Tue 2/1/22	Fri 2/4/22	136
138		1.9.4	Run conduit fire suppression system	2 days	Fri 2/4/22	Tue 2/8/22	137
139		1.9.5	Run conduit for parking lot control system	3 days	Tue 2/8/22	Fri 2/11/22	138
140		1.9.6	Pull wires to all parking deck locations	9 days	Fri 2/11/22	Mon 5/23/22	139
141		1.9.7	Run retail electrical	3 days	Mon 5/23/22	Thu 5/26/22	140
142		1.9.8	Run conduit and wire f8				

ID	 Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors
153		1.12.2	Form retail roadside staircase	5 days	Thu 2/10/22	Thu 2/17/22	152
154		1.12.3	Pour retail roadside retail staircase	2 days	Thu 2/17/22		



F | S | S | M | T

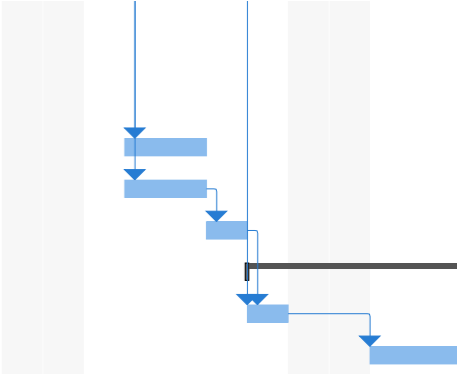

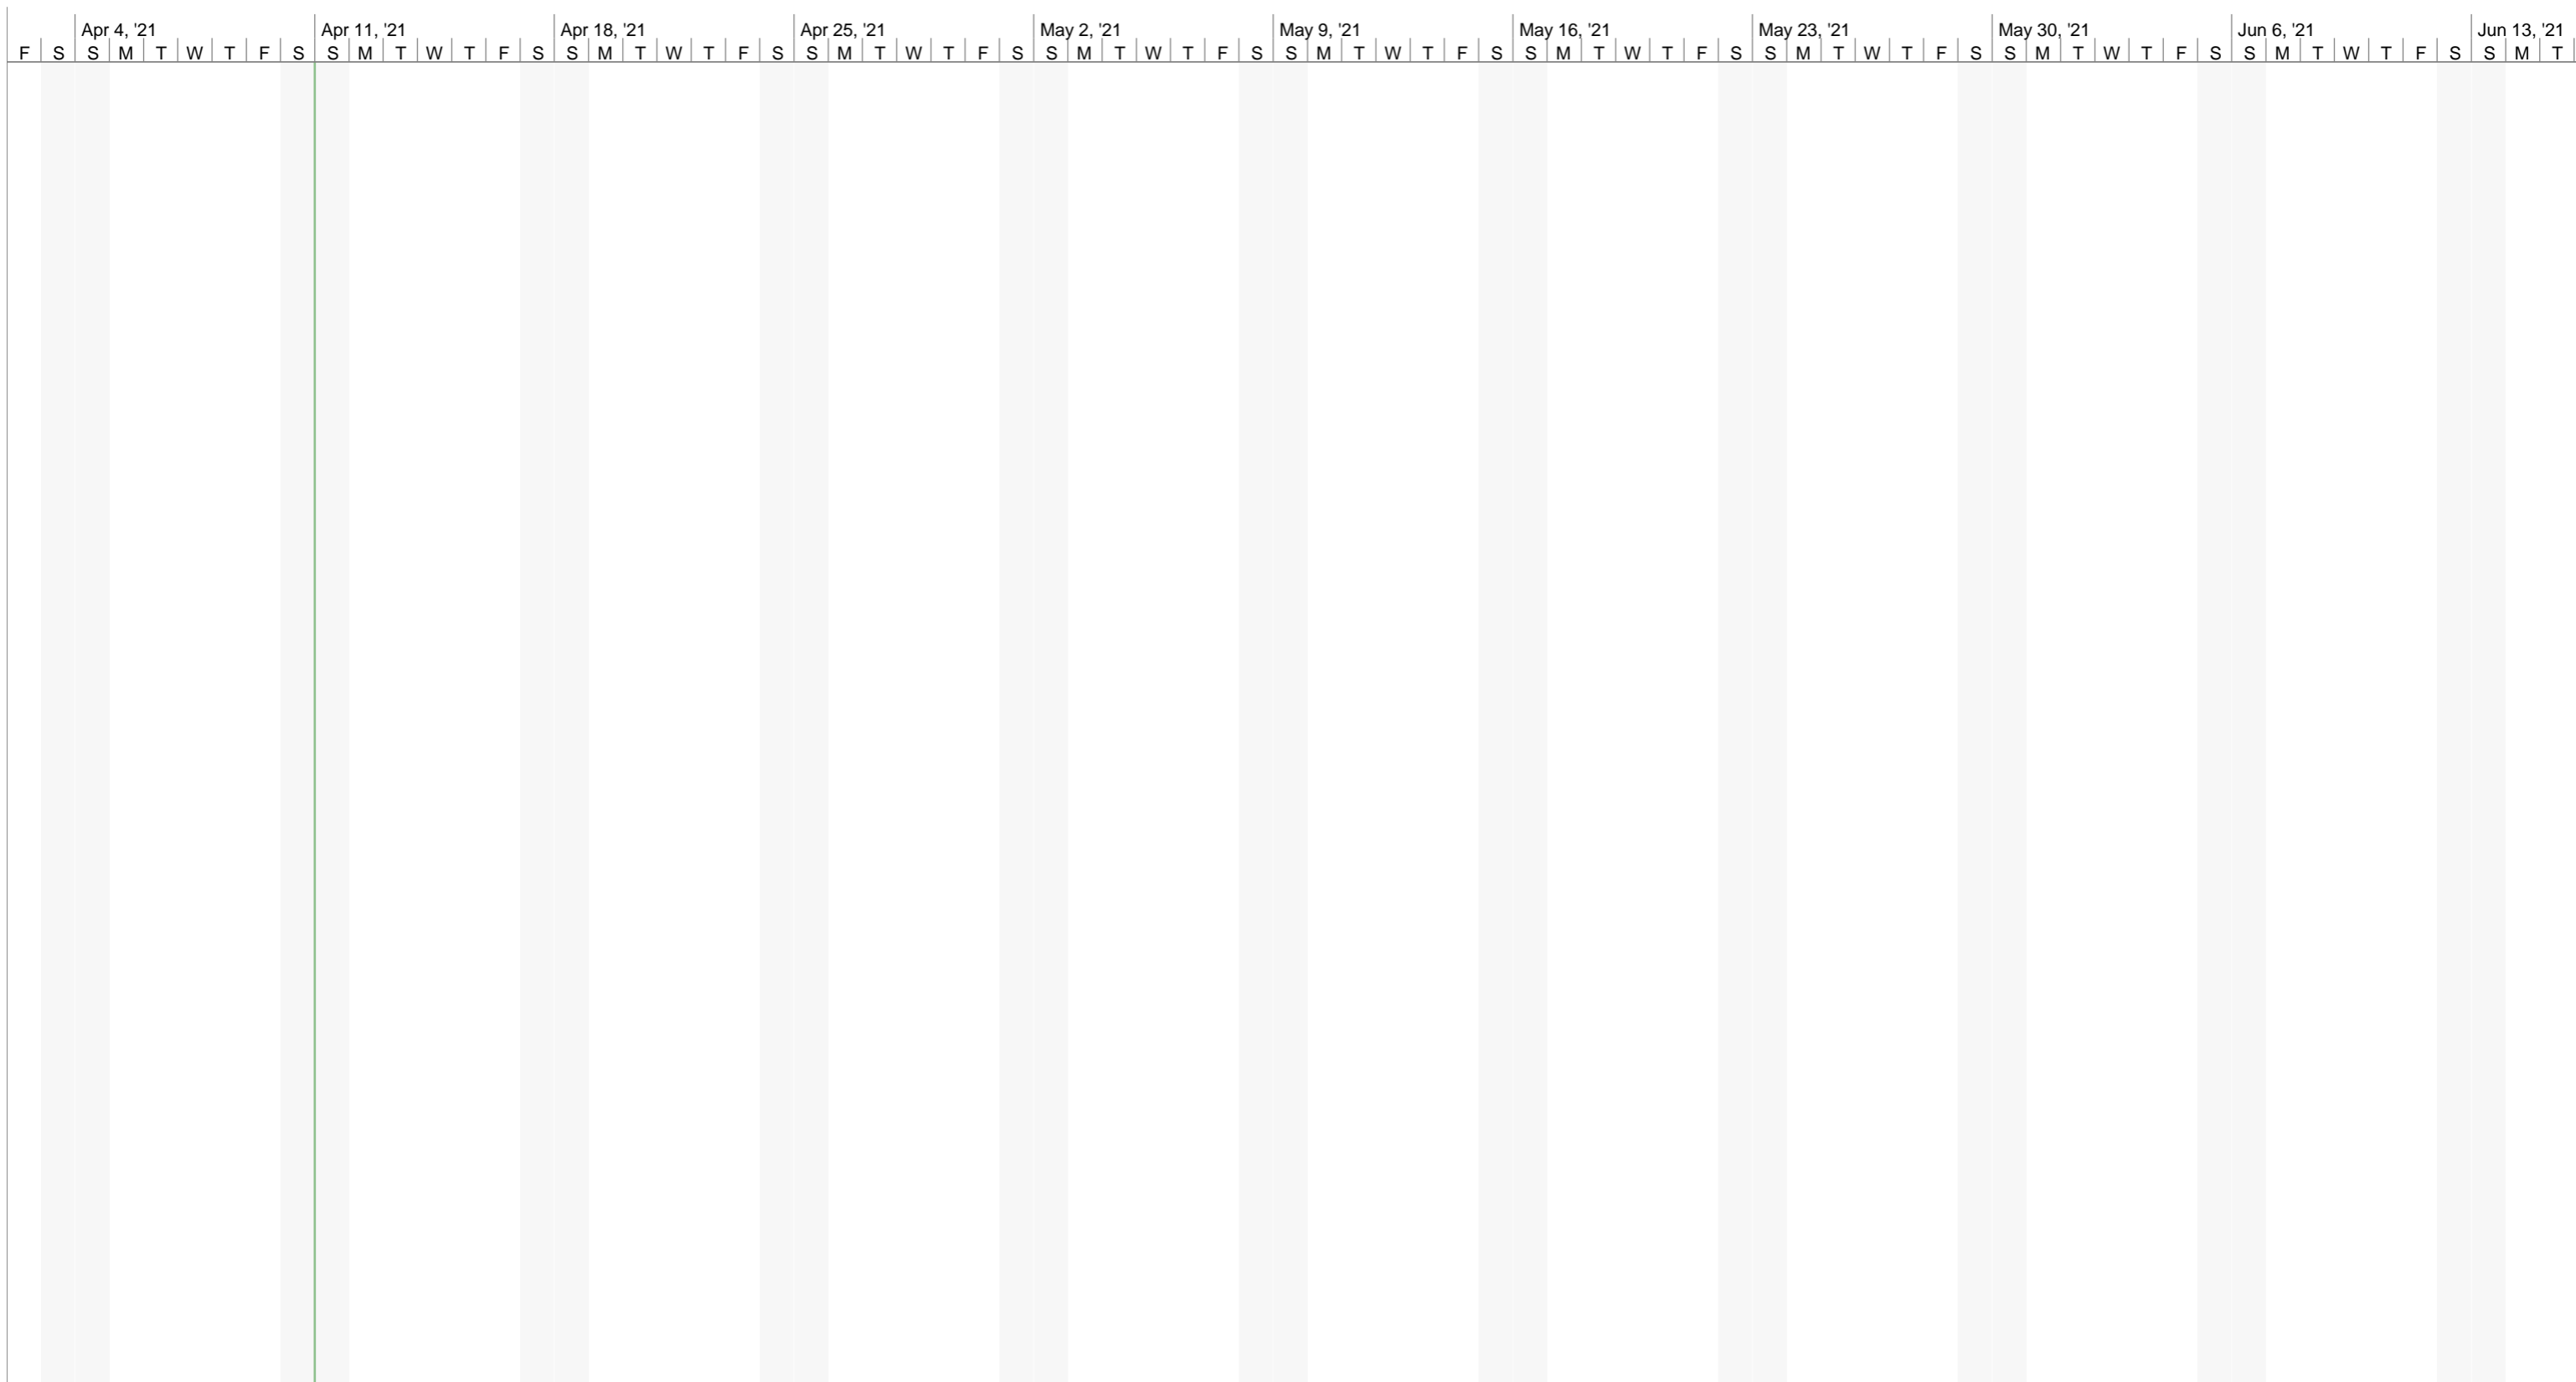

Task




Split



Milestone



Sumo8 51.84 Td [(S)-5 (um)-5 (o8 51.84 Td [(S)-5 (um)-5 (1.64 626.52 re W* n q 1 0 0 1 21.84 124.22 cm 0.502 G 0.48 w 1 j 0 0 m 1151.641.84 Td [(S)-5 (um)-5 (1.64 626.52 re W* n q 1.,52 re 0 0 m 3.24 -3.24 | 0 -6.48 | -3.24 -3.24 | h [(S)-5 Q q 2422 30.48 w 1 j 0 0 m 1151.64 (

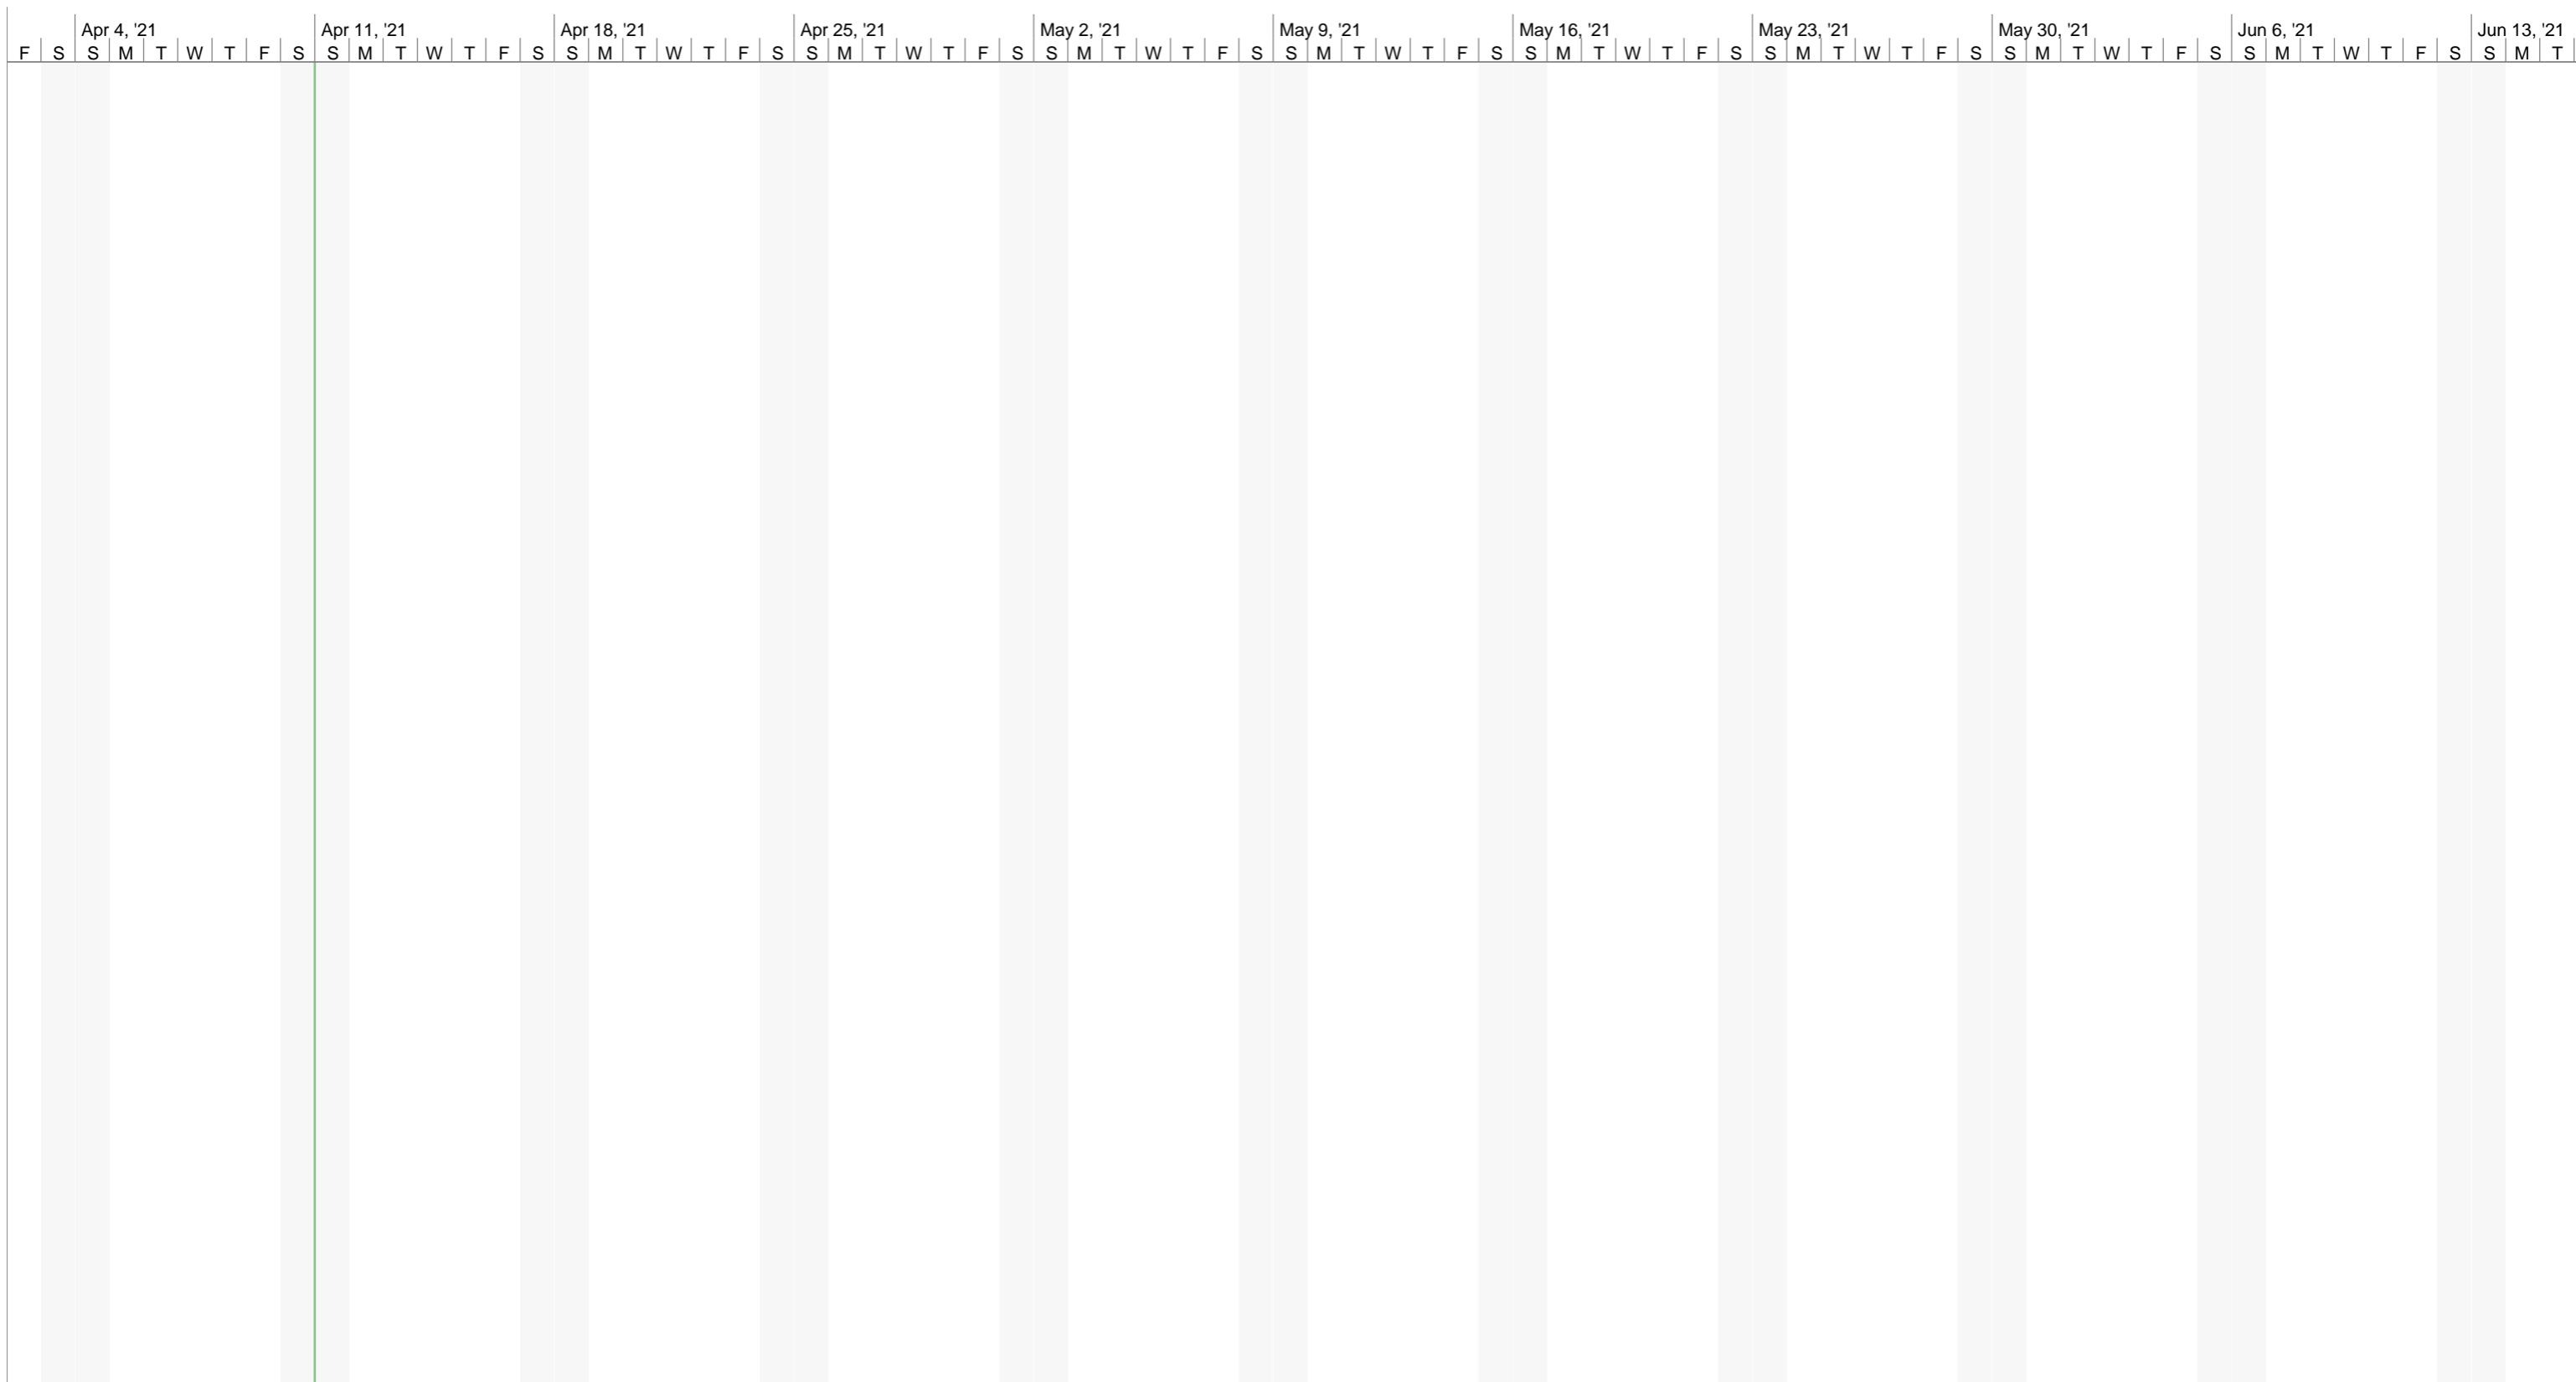

Task



Split




Milestone




Sumo8 51.84 Td [(S)-5 (um)-5 (o8 51.84 Td [(S)-5 (um)-5 (1.64 626.52 re W* n q 1 0 0 1 21.84 124.22 cm 0.502 G 0.48 w 1 j 0 0 m 1151.641.84 Td [(S)-5 (um)-5 (1.64 626.52 re W* n q 1.,52 re 0 0 m 3.24 -3.24 | 0 -6.48 | -3.24 -3.24 | h [(S)-5 Q q 2422 30.48 w 1 j 0 0 m 1151.64 (


W T F S Jun 20, '21 S M T W T F S Jun 27, '21 S M T W T F S Jul 4, '21 S M T W T F S Jul 11, '21 S M T W T F S Jul 18, '21 S M T W T F S Jul 25, '21 S M T W T F S Aug 1, '21 S M T W T F S Aug 8, '21 S M T W T F S Aug 15, '21 S M T W T F S Aug 22, '21 Aug

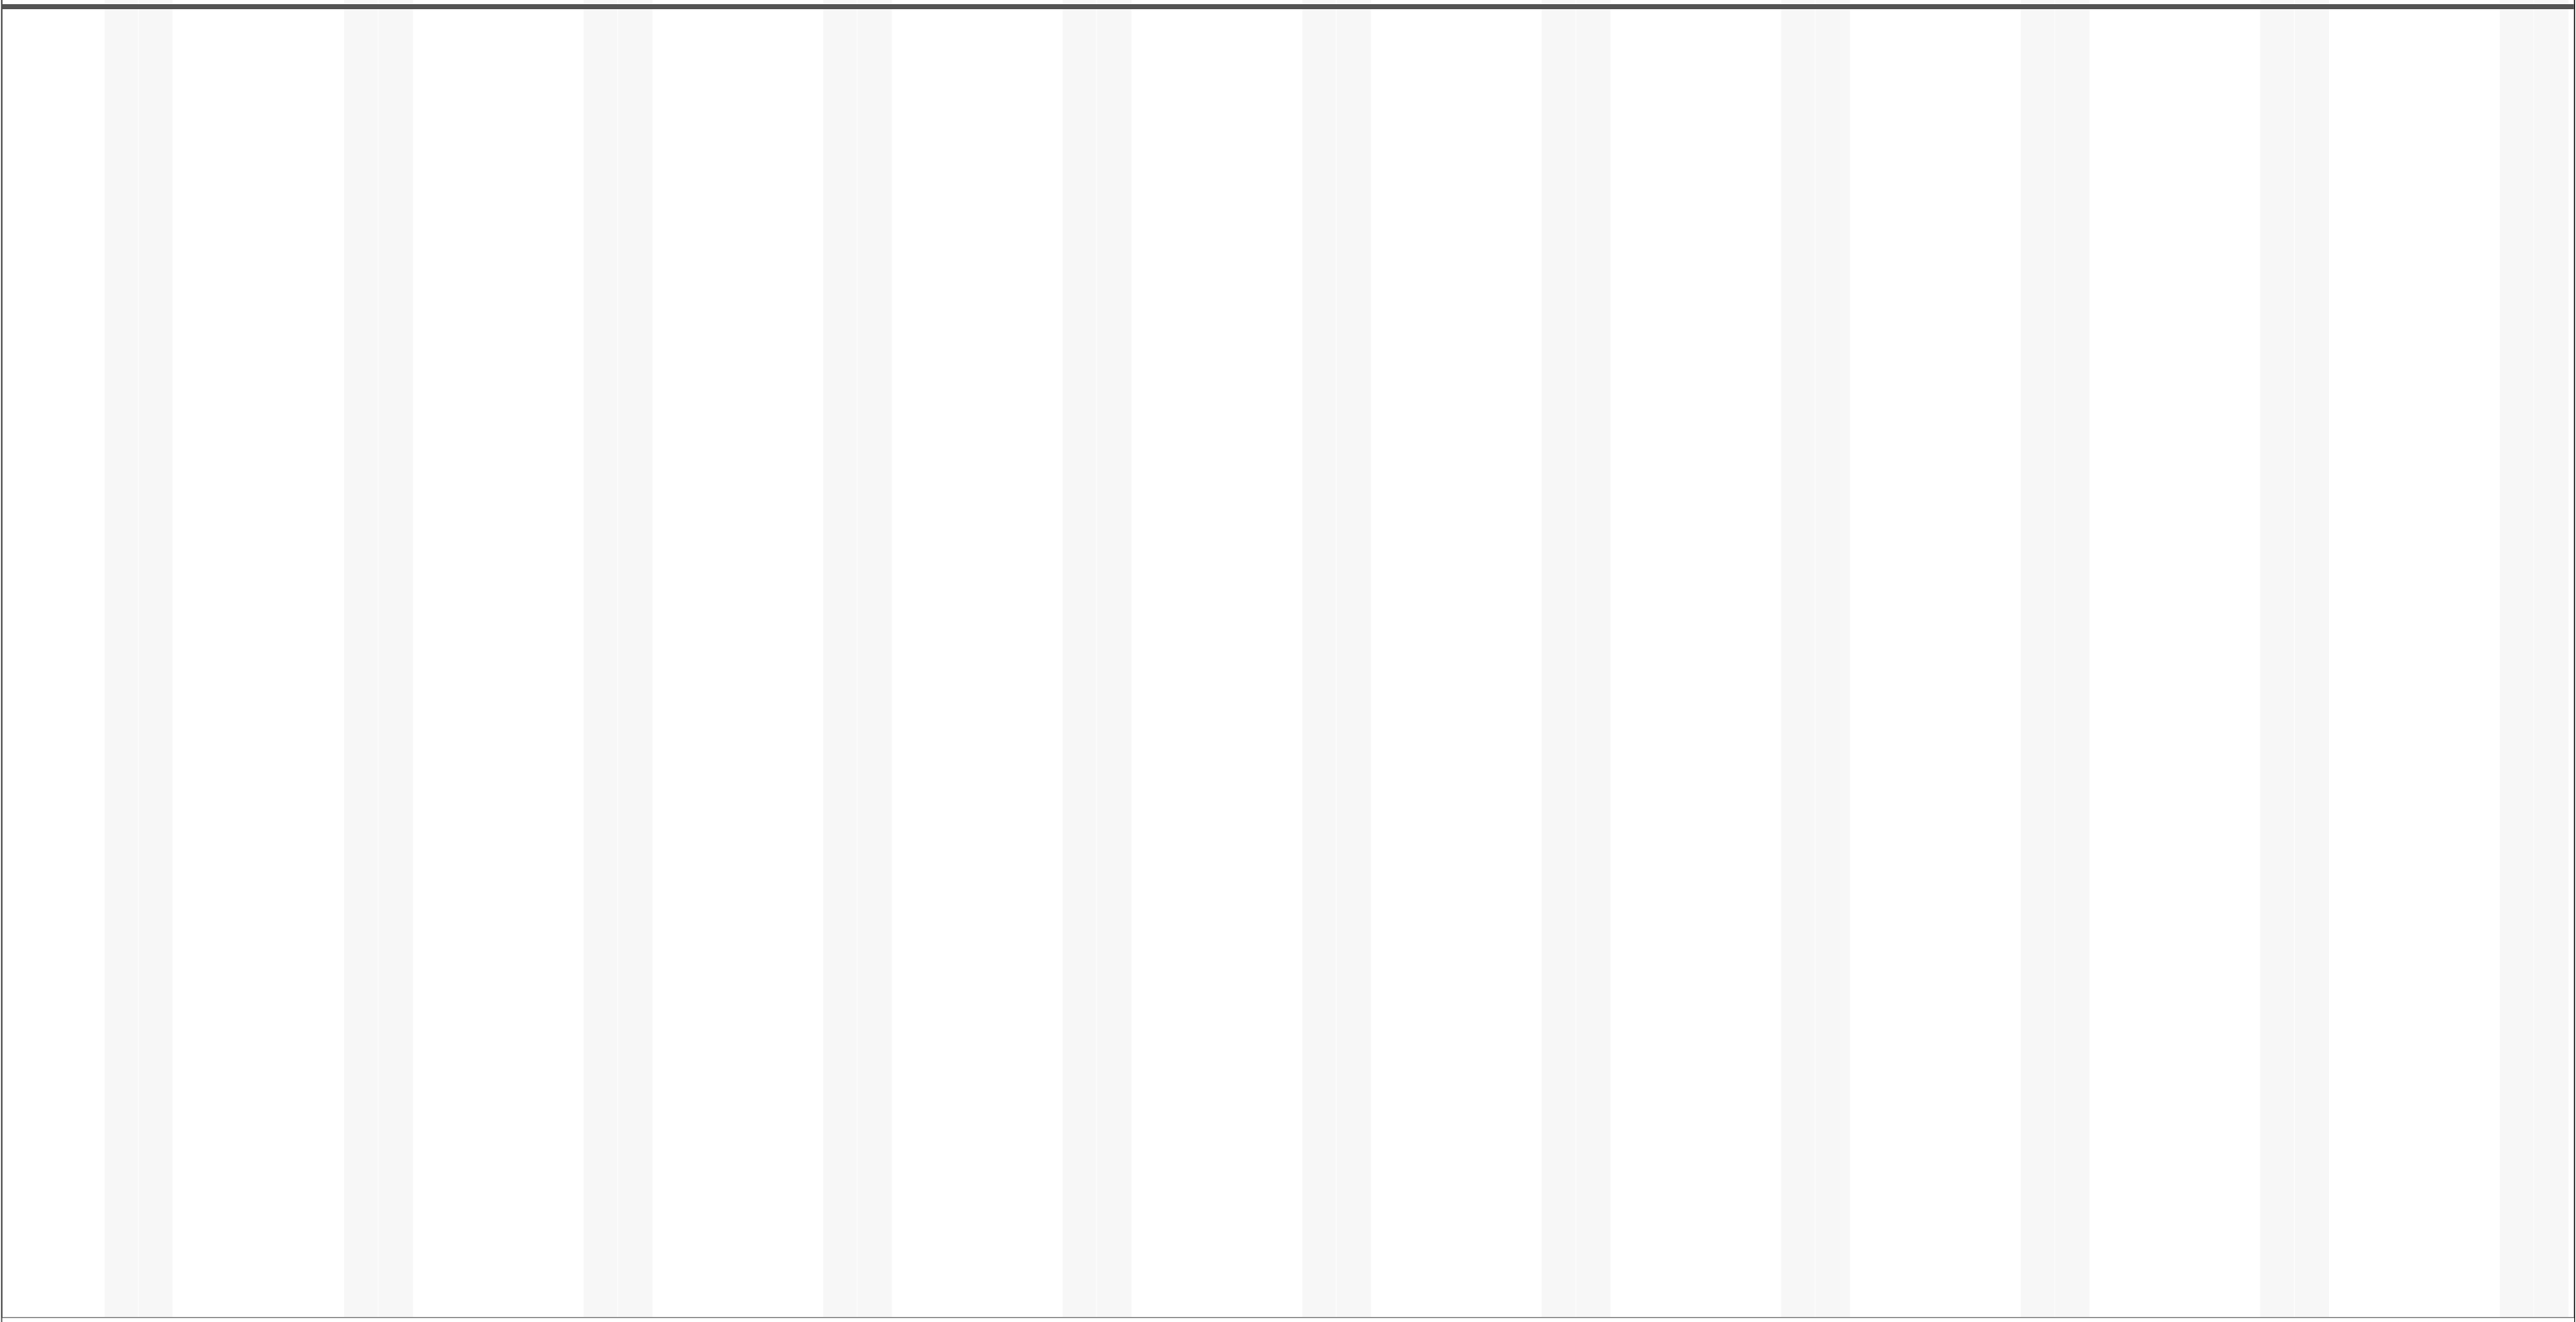


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

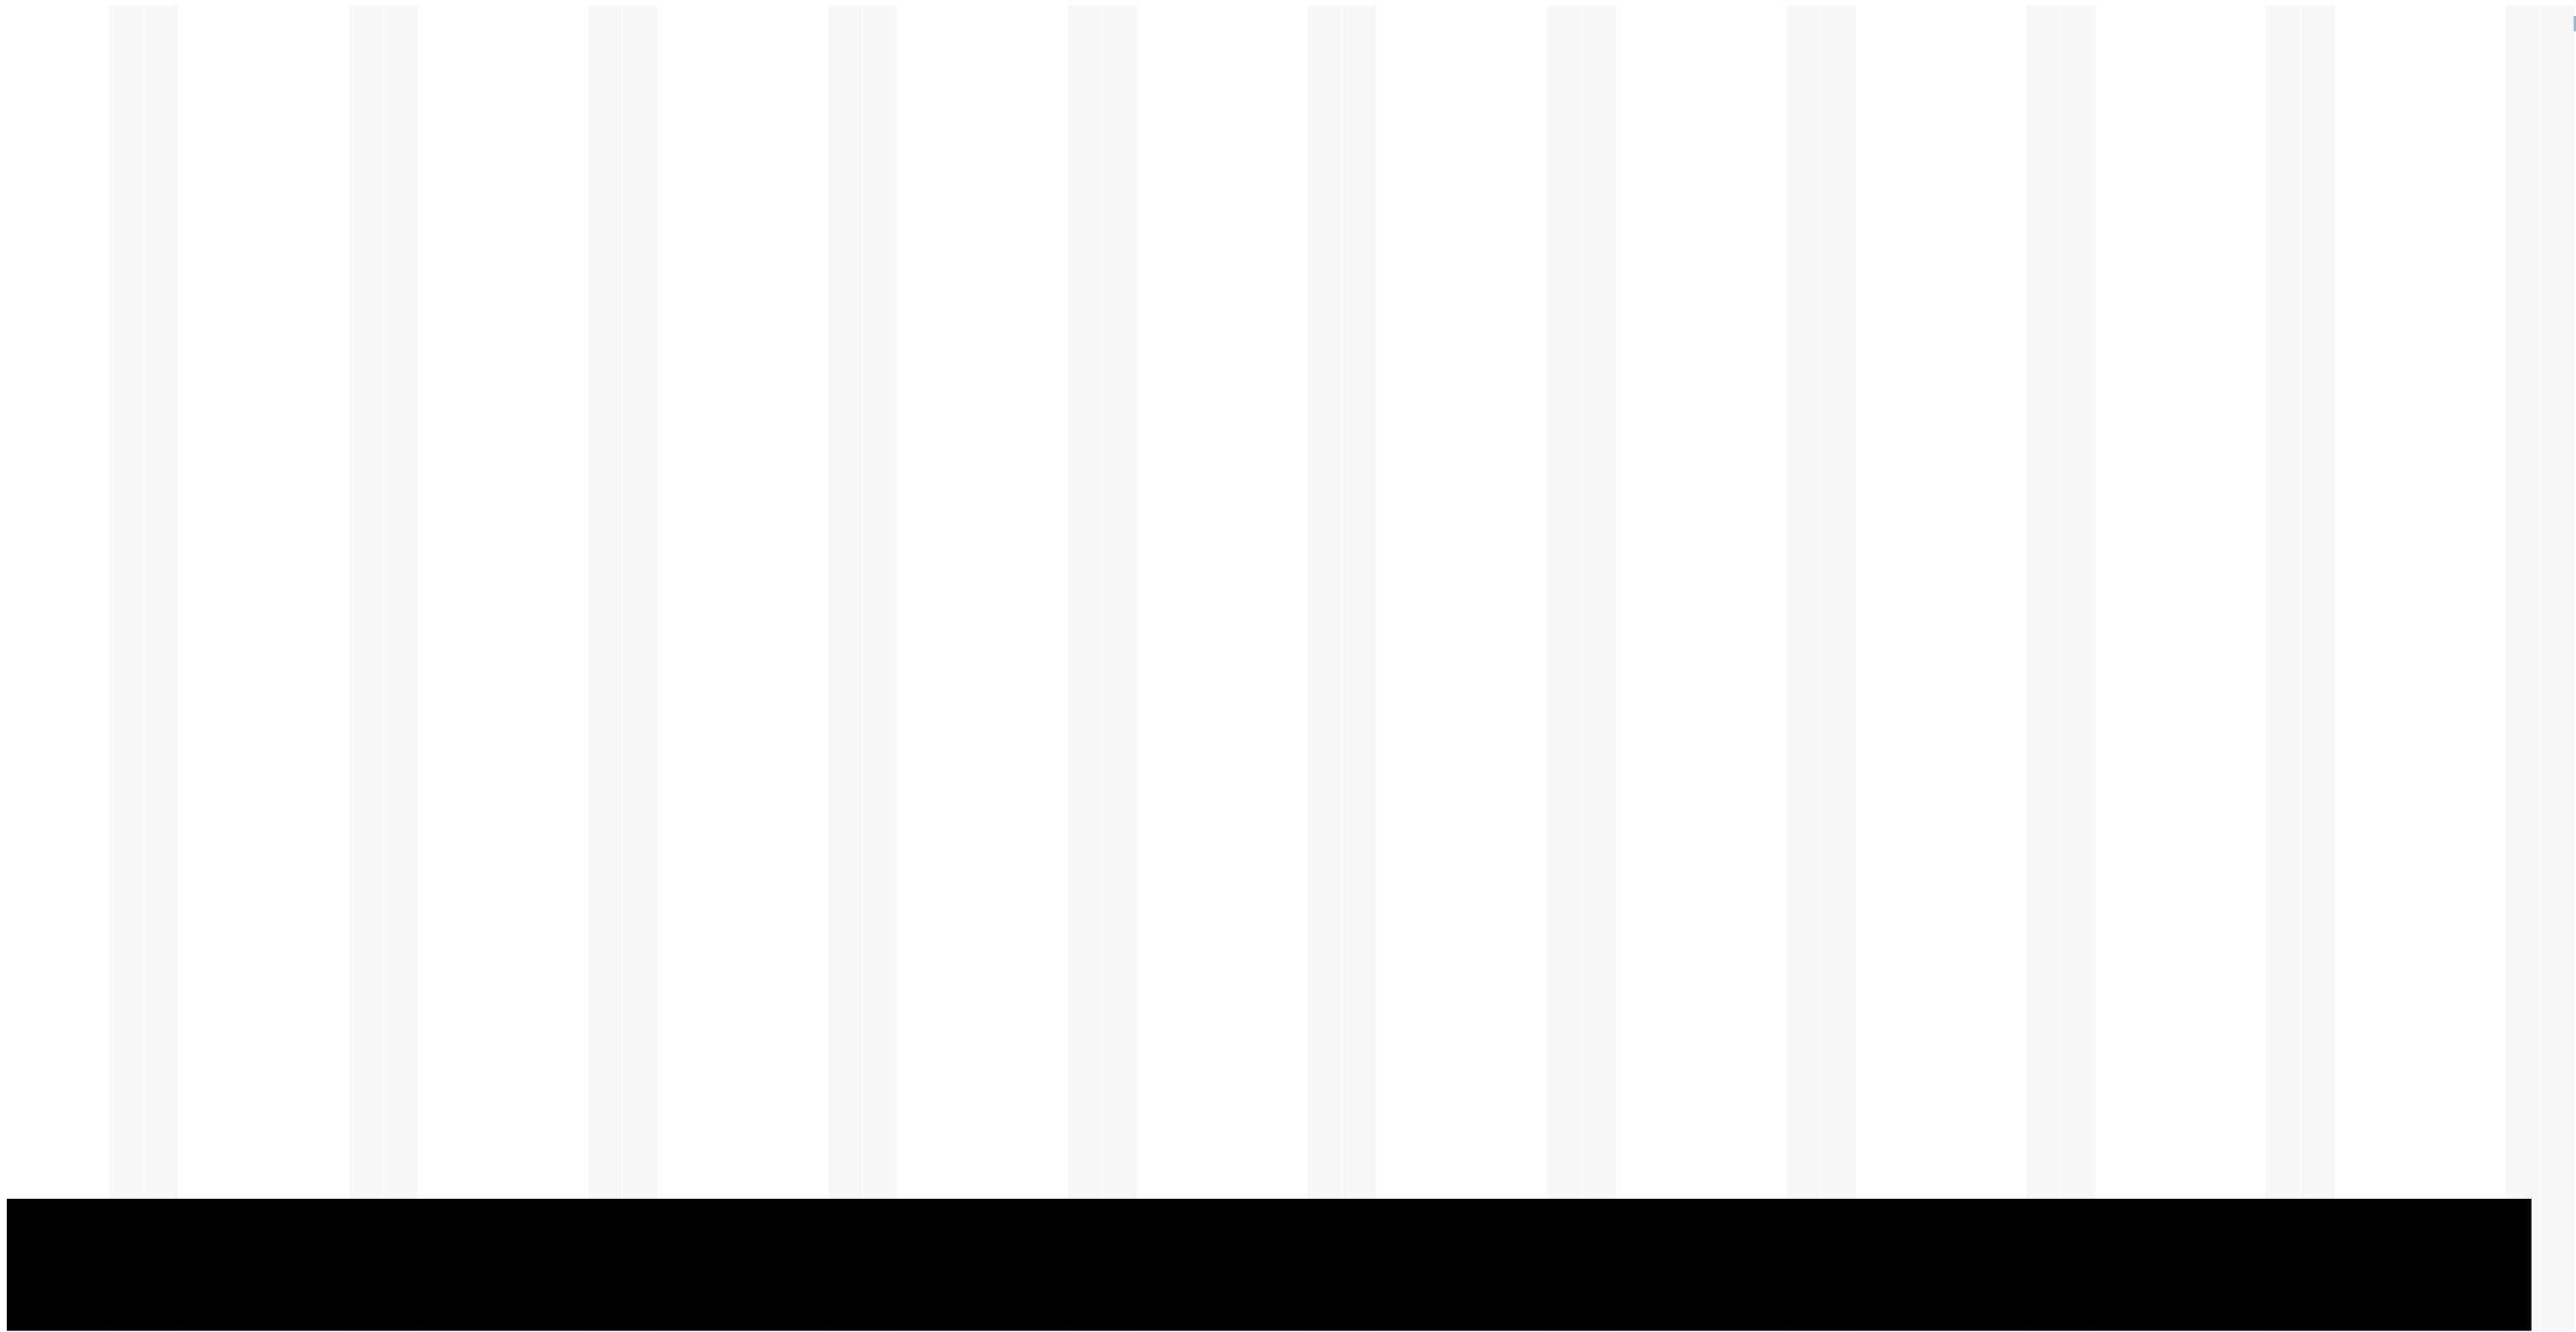

W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | **W** | T | F | S | S | M |

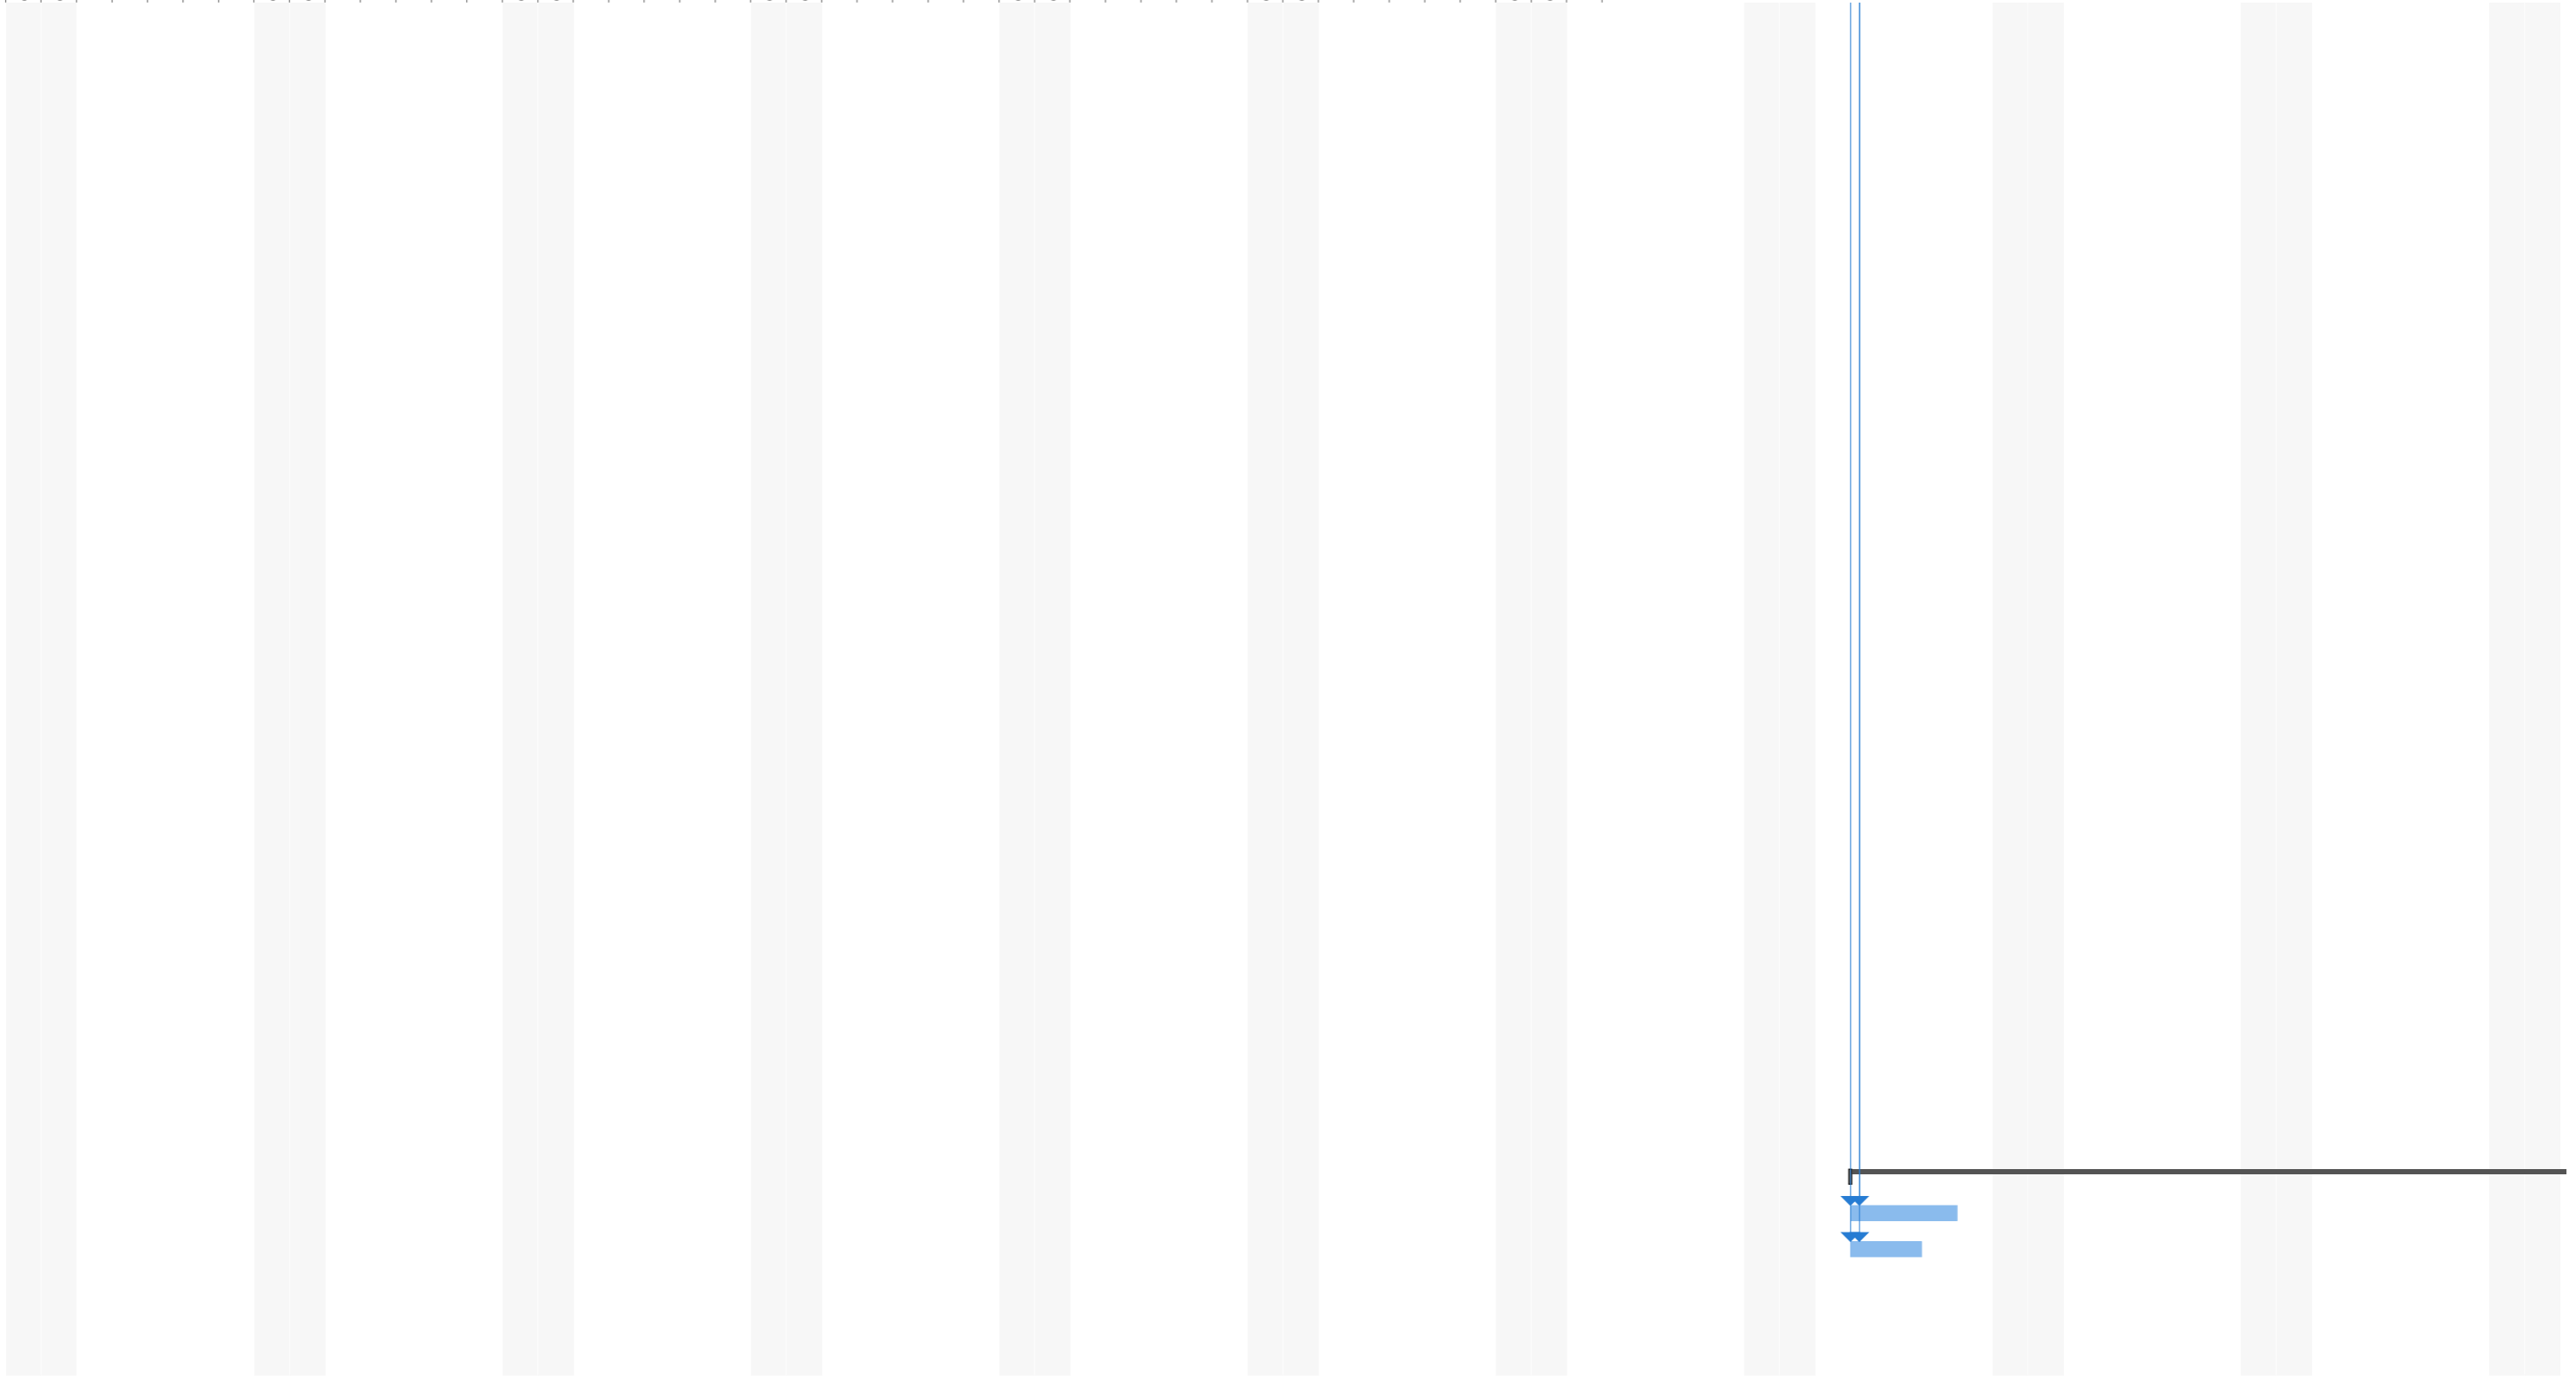


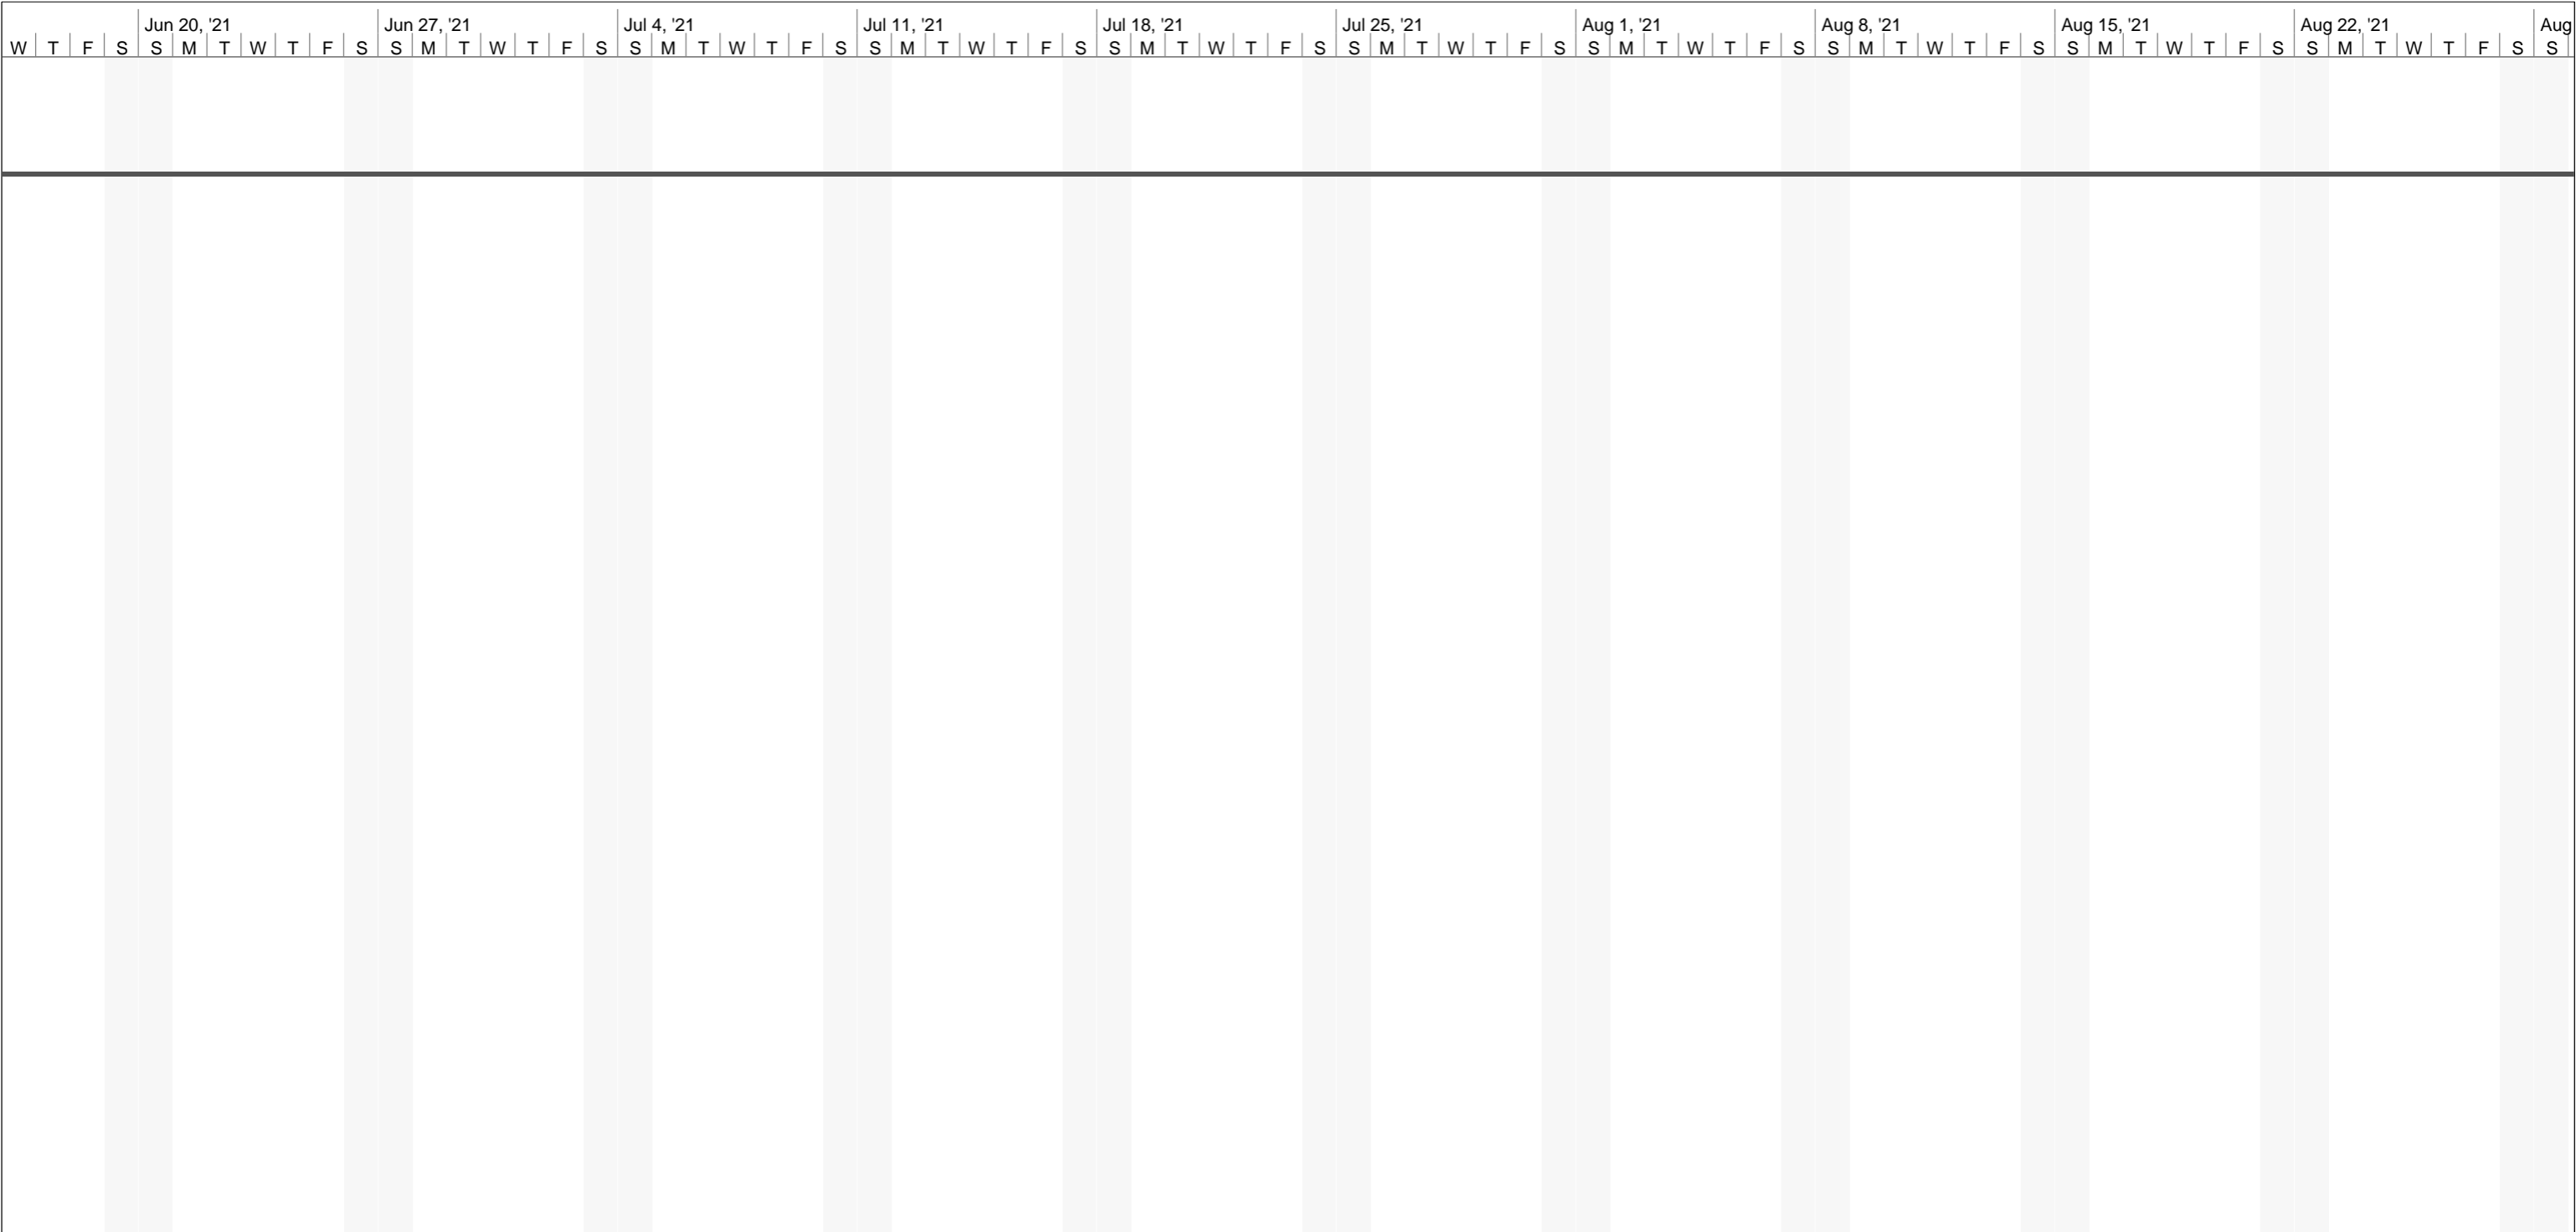






Project: Parking garage schedu
Date: Sun 4/11/21

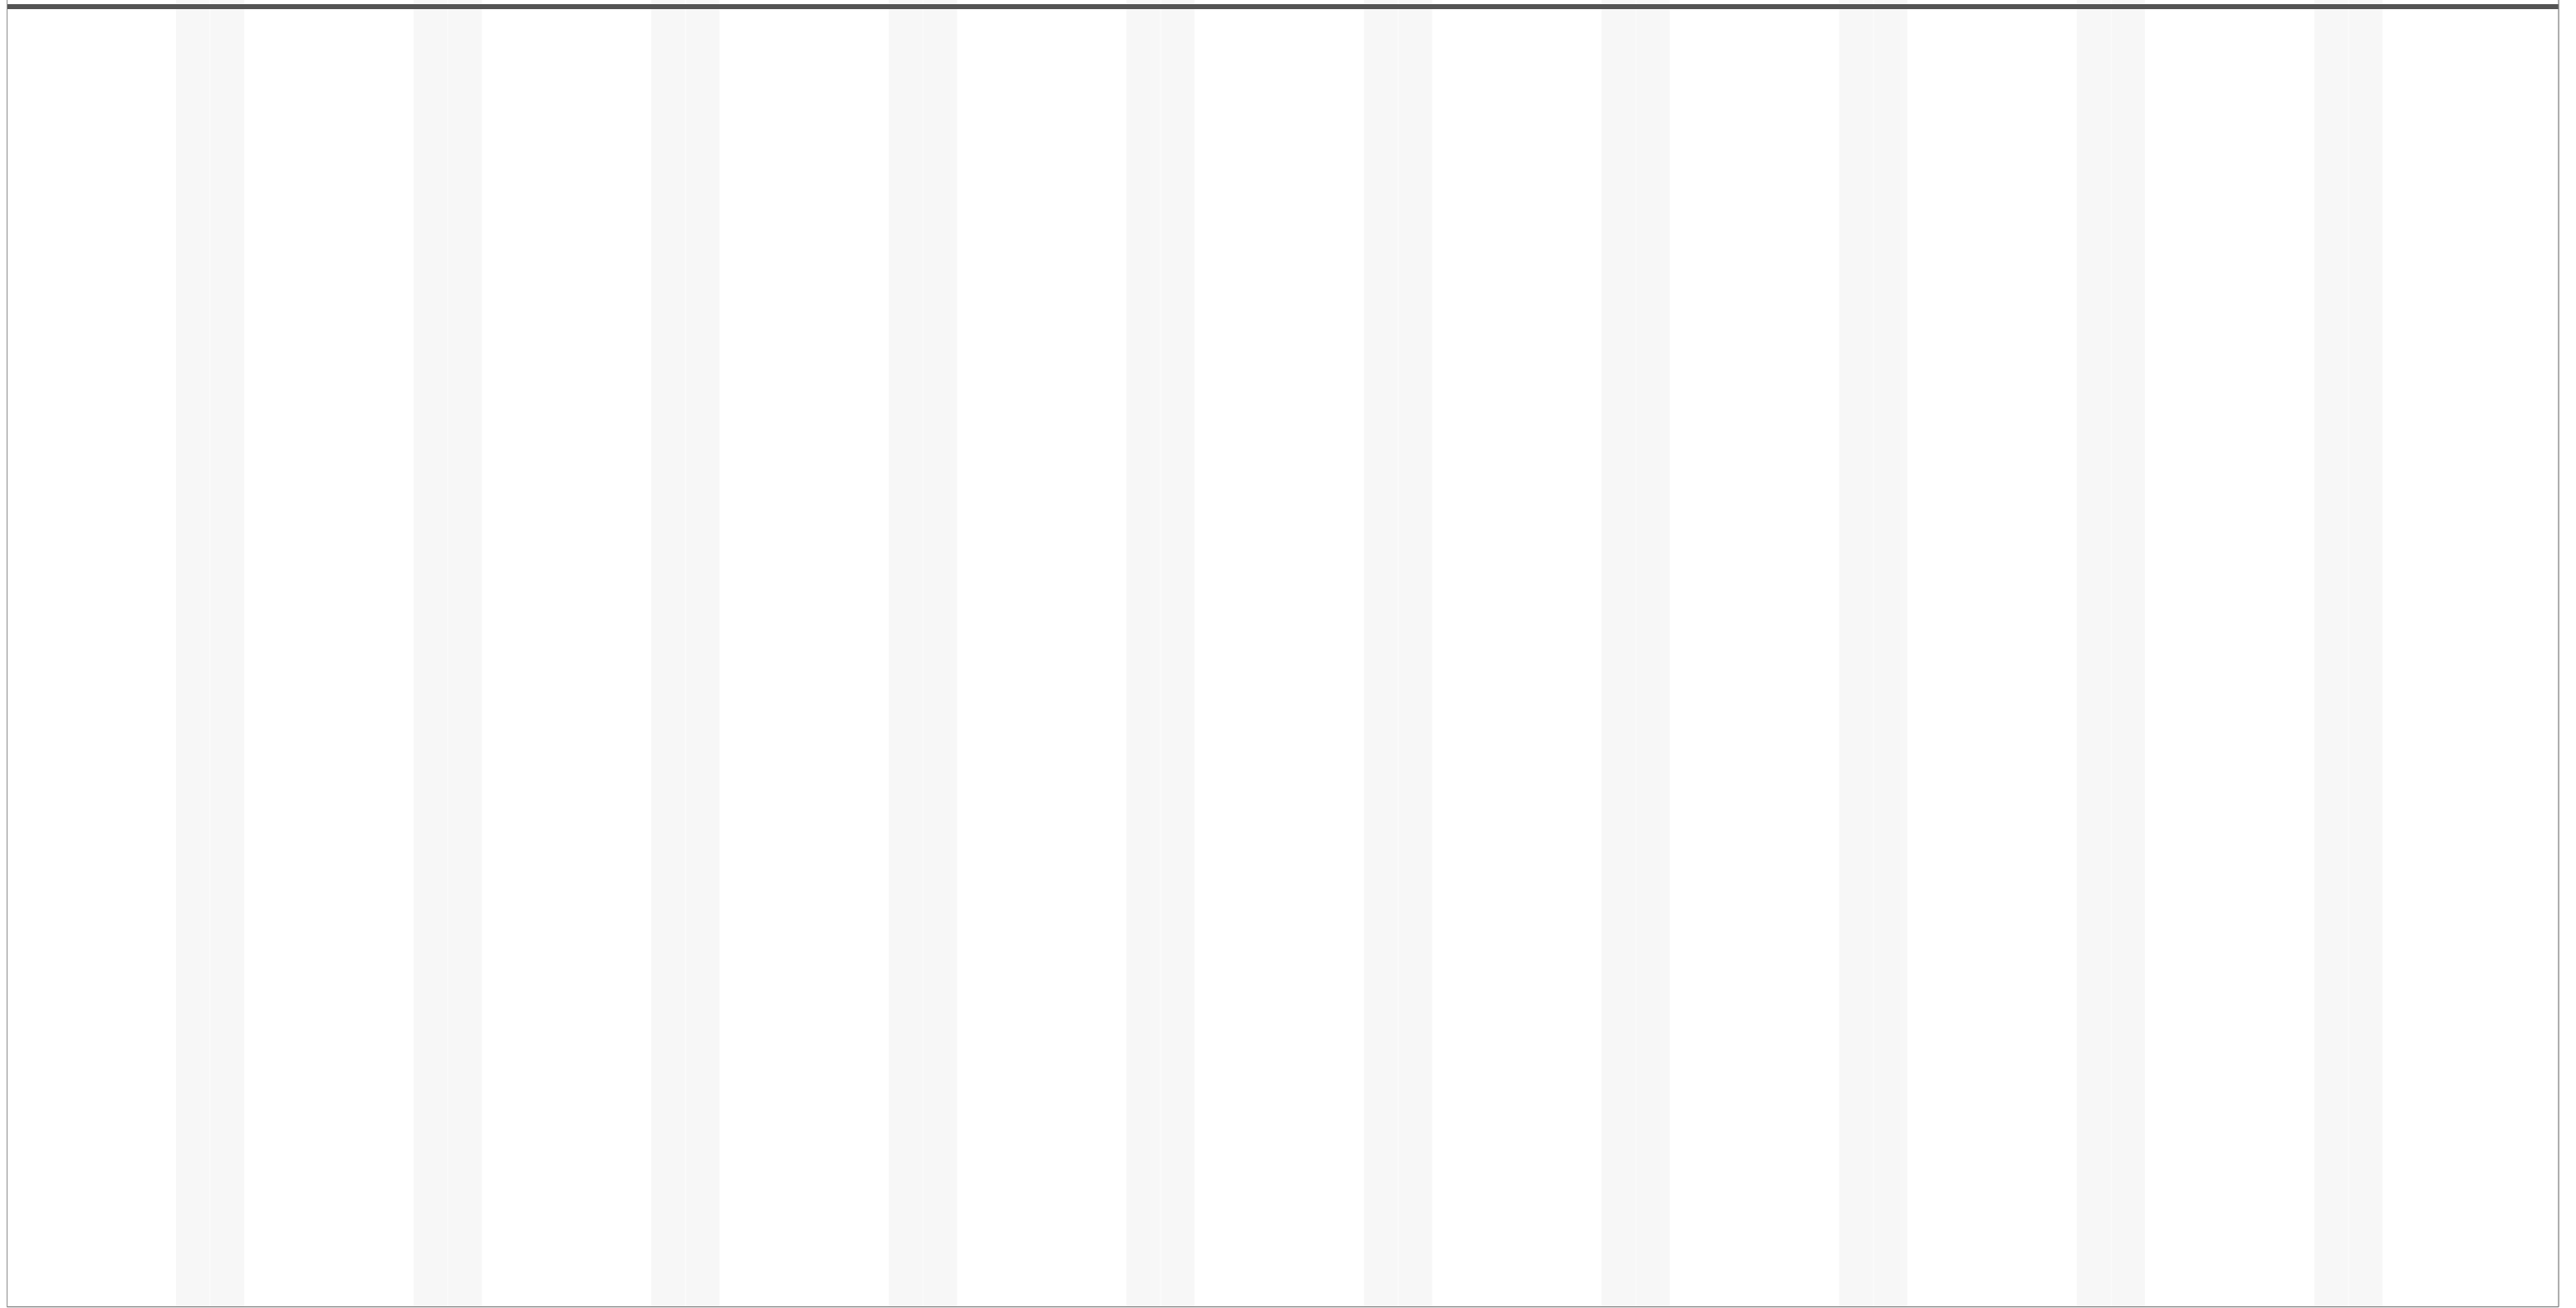Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


29, '21 | M | T | W | T | F | S | Sep 5, '21 | S | M | T | W | T | F | S | Sep 12, '21 | S | M | T | W | T | F | S | Sep 19, '21 | S | M | T | W | T | F | S | Sep 26, '21 | S | M | T | W | T | F | S | Oct 3, '21 | S | M | T | W | T | F | S | Oct 10, '21 | S | M | T | W | T | F | S | Oct 17, '21 | S | M | T | W | T | F | S | Oct 24, '21 | S | M | T | W | T | F | S | Oct 31, '21 | S | M | T | W | T | F | S | Nov 7, '21 | S | M | T | W | T | F | S



- Task 
- Split 
- Milestone 
- Summary 

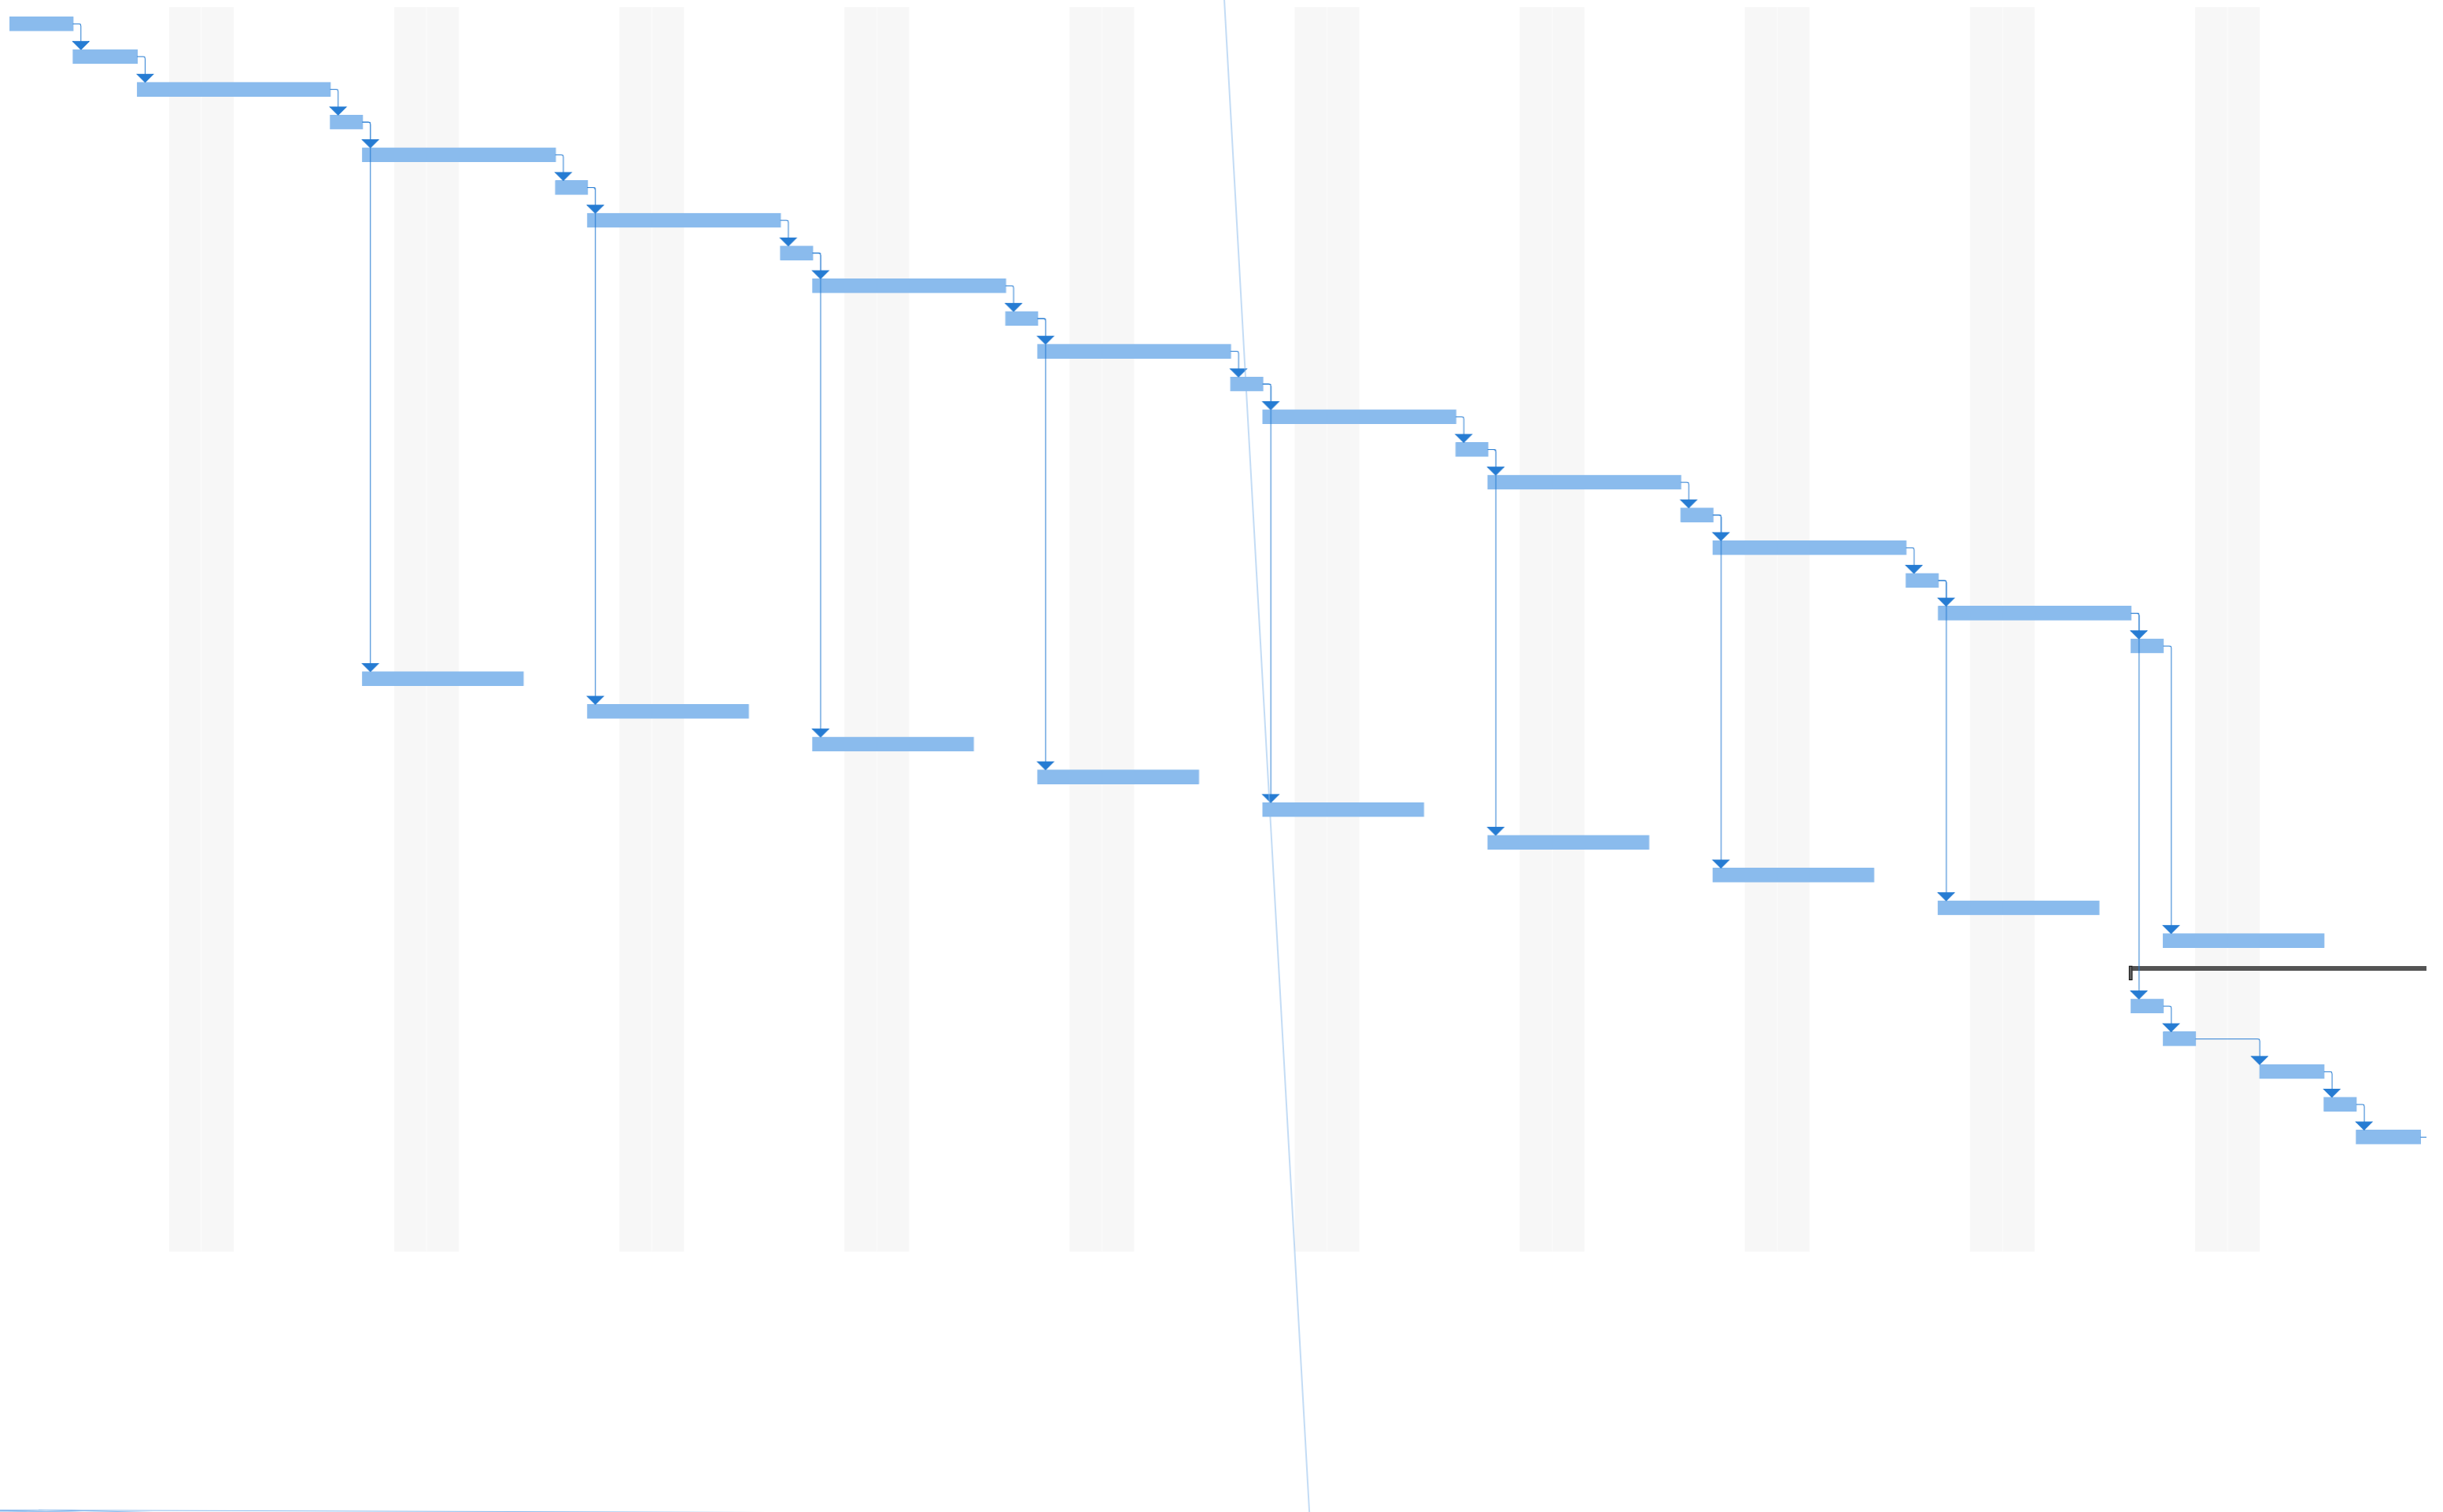


29, '21 M T W T F S Sep 5, '21 S M T W T F S Sep 12, '21 S M T W T F S Sep 19, '21 S M T W T F S Sep 26, '21 S M T W T F S Oct 3, '21 S M T W T F S Oct 10, '21 S M T W T F S Oct 17, '21 S M T W T F S Oct 24, '21 S M T W T F S Oct 31, '21 S M T W T F S Nov 7, '21 S M T W T F S

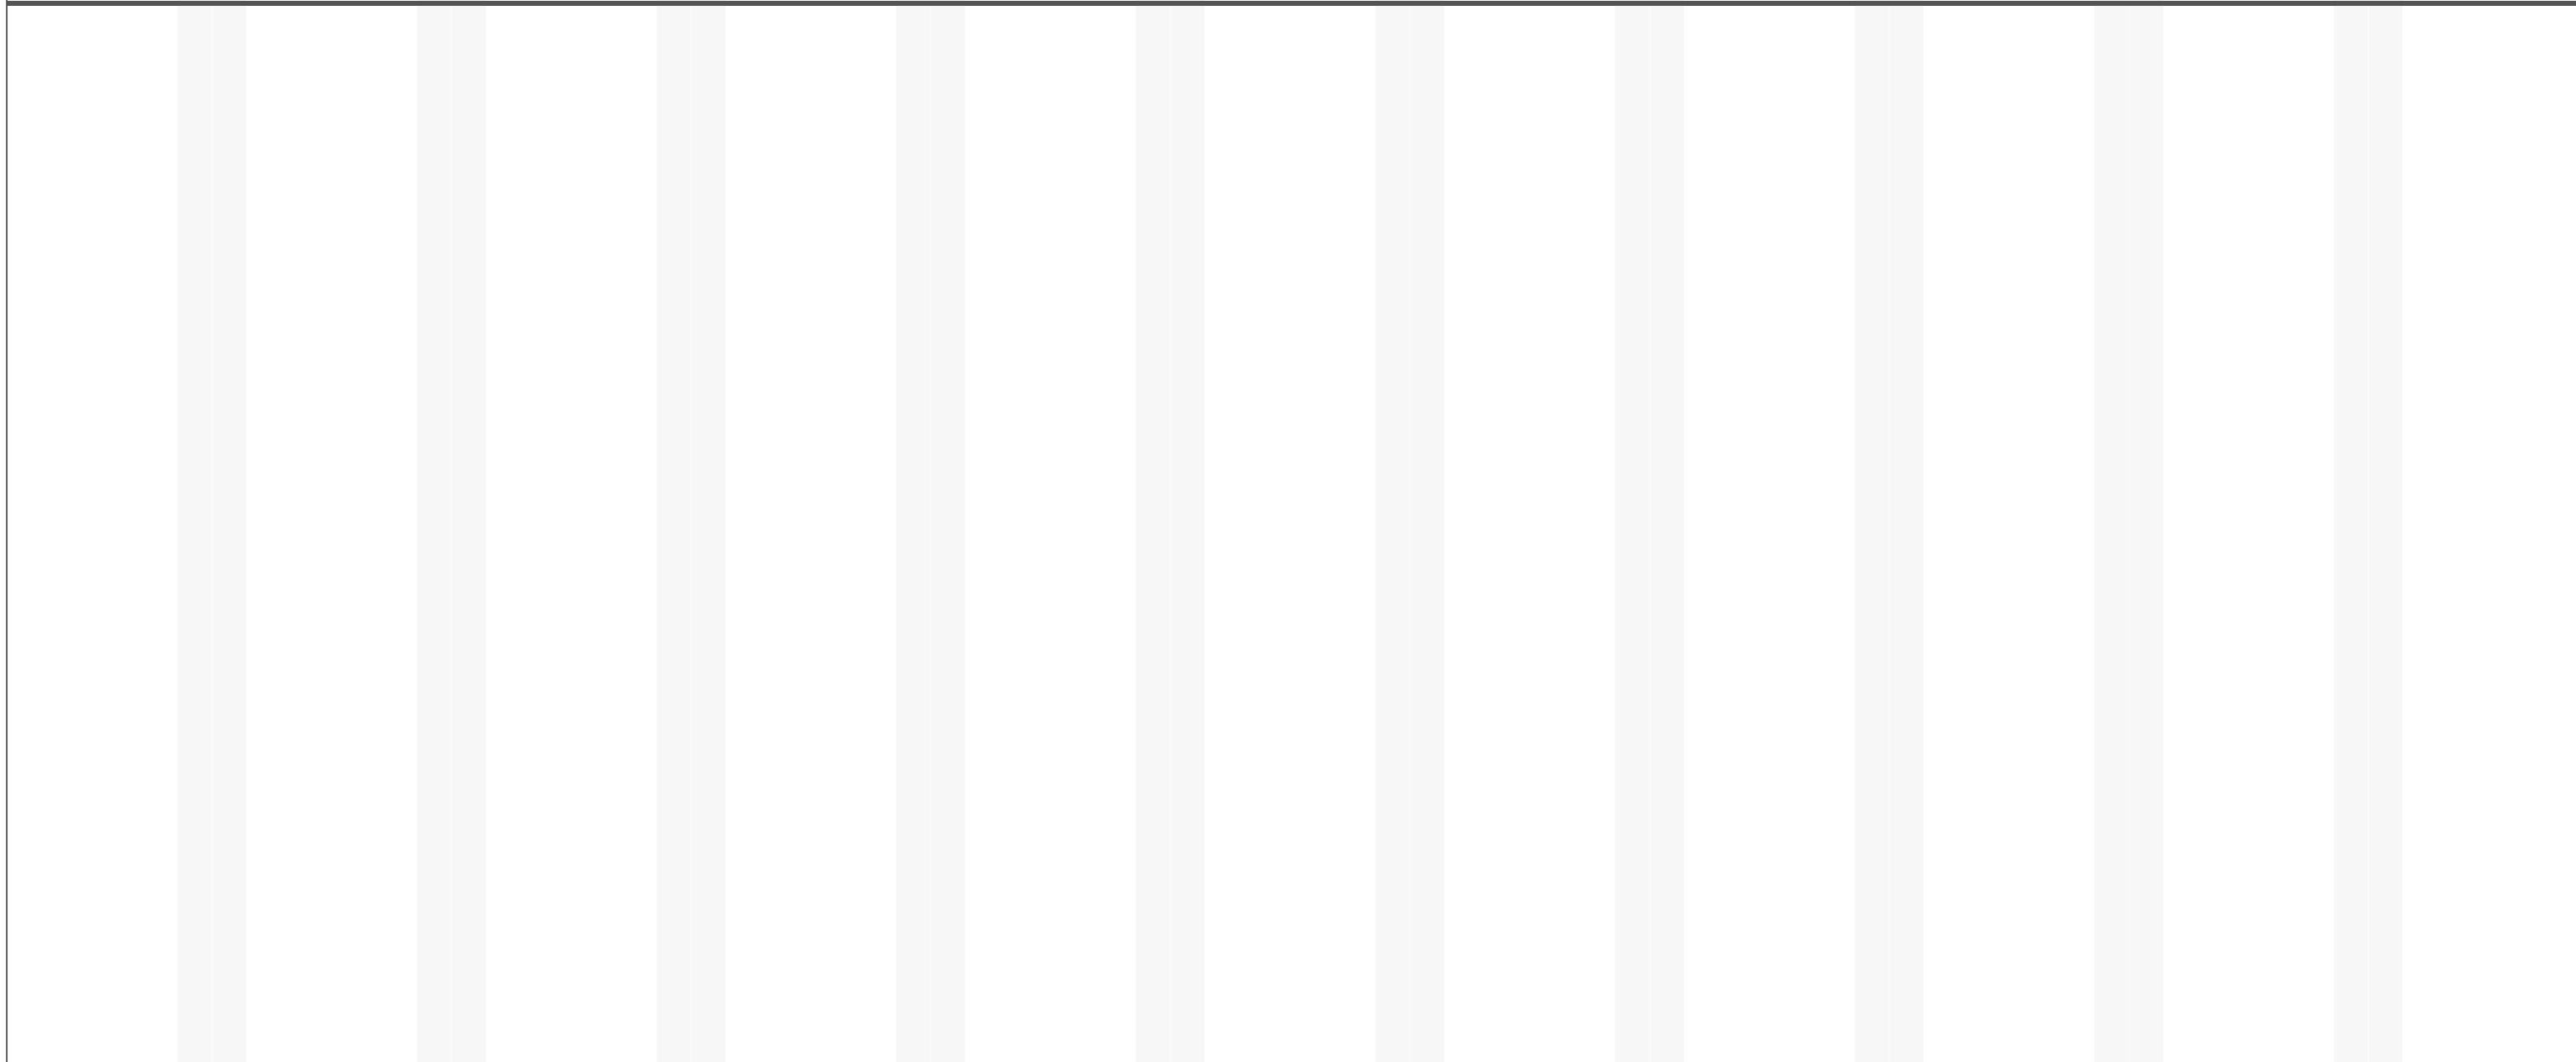


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

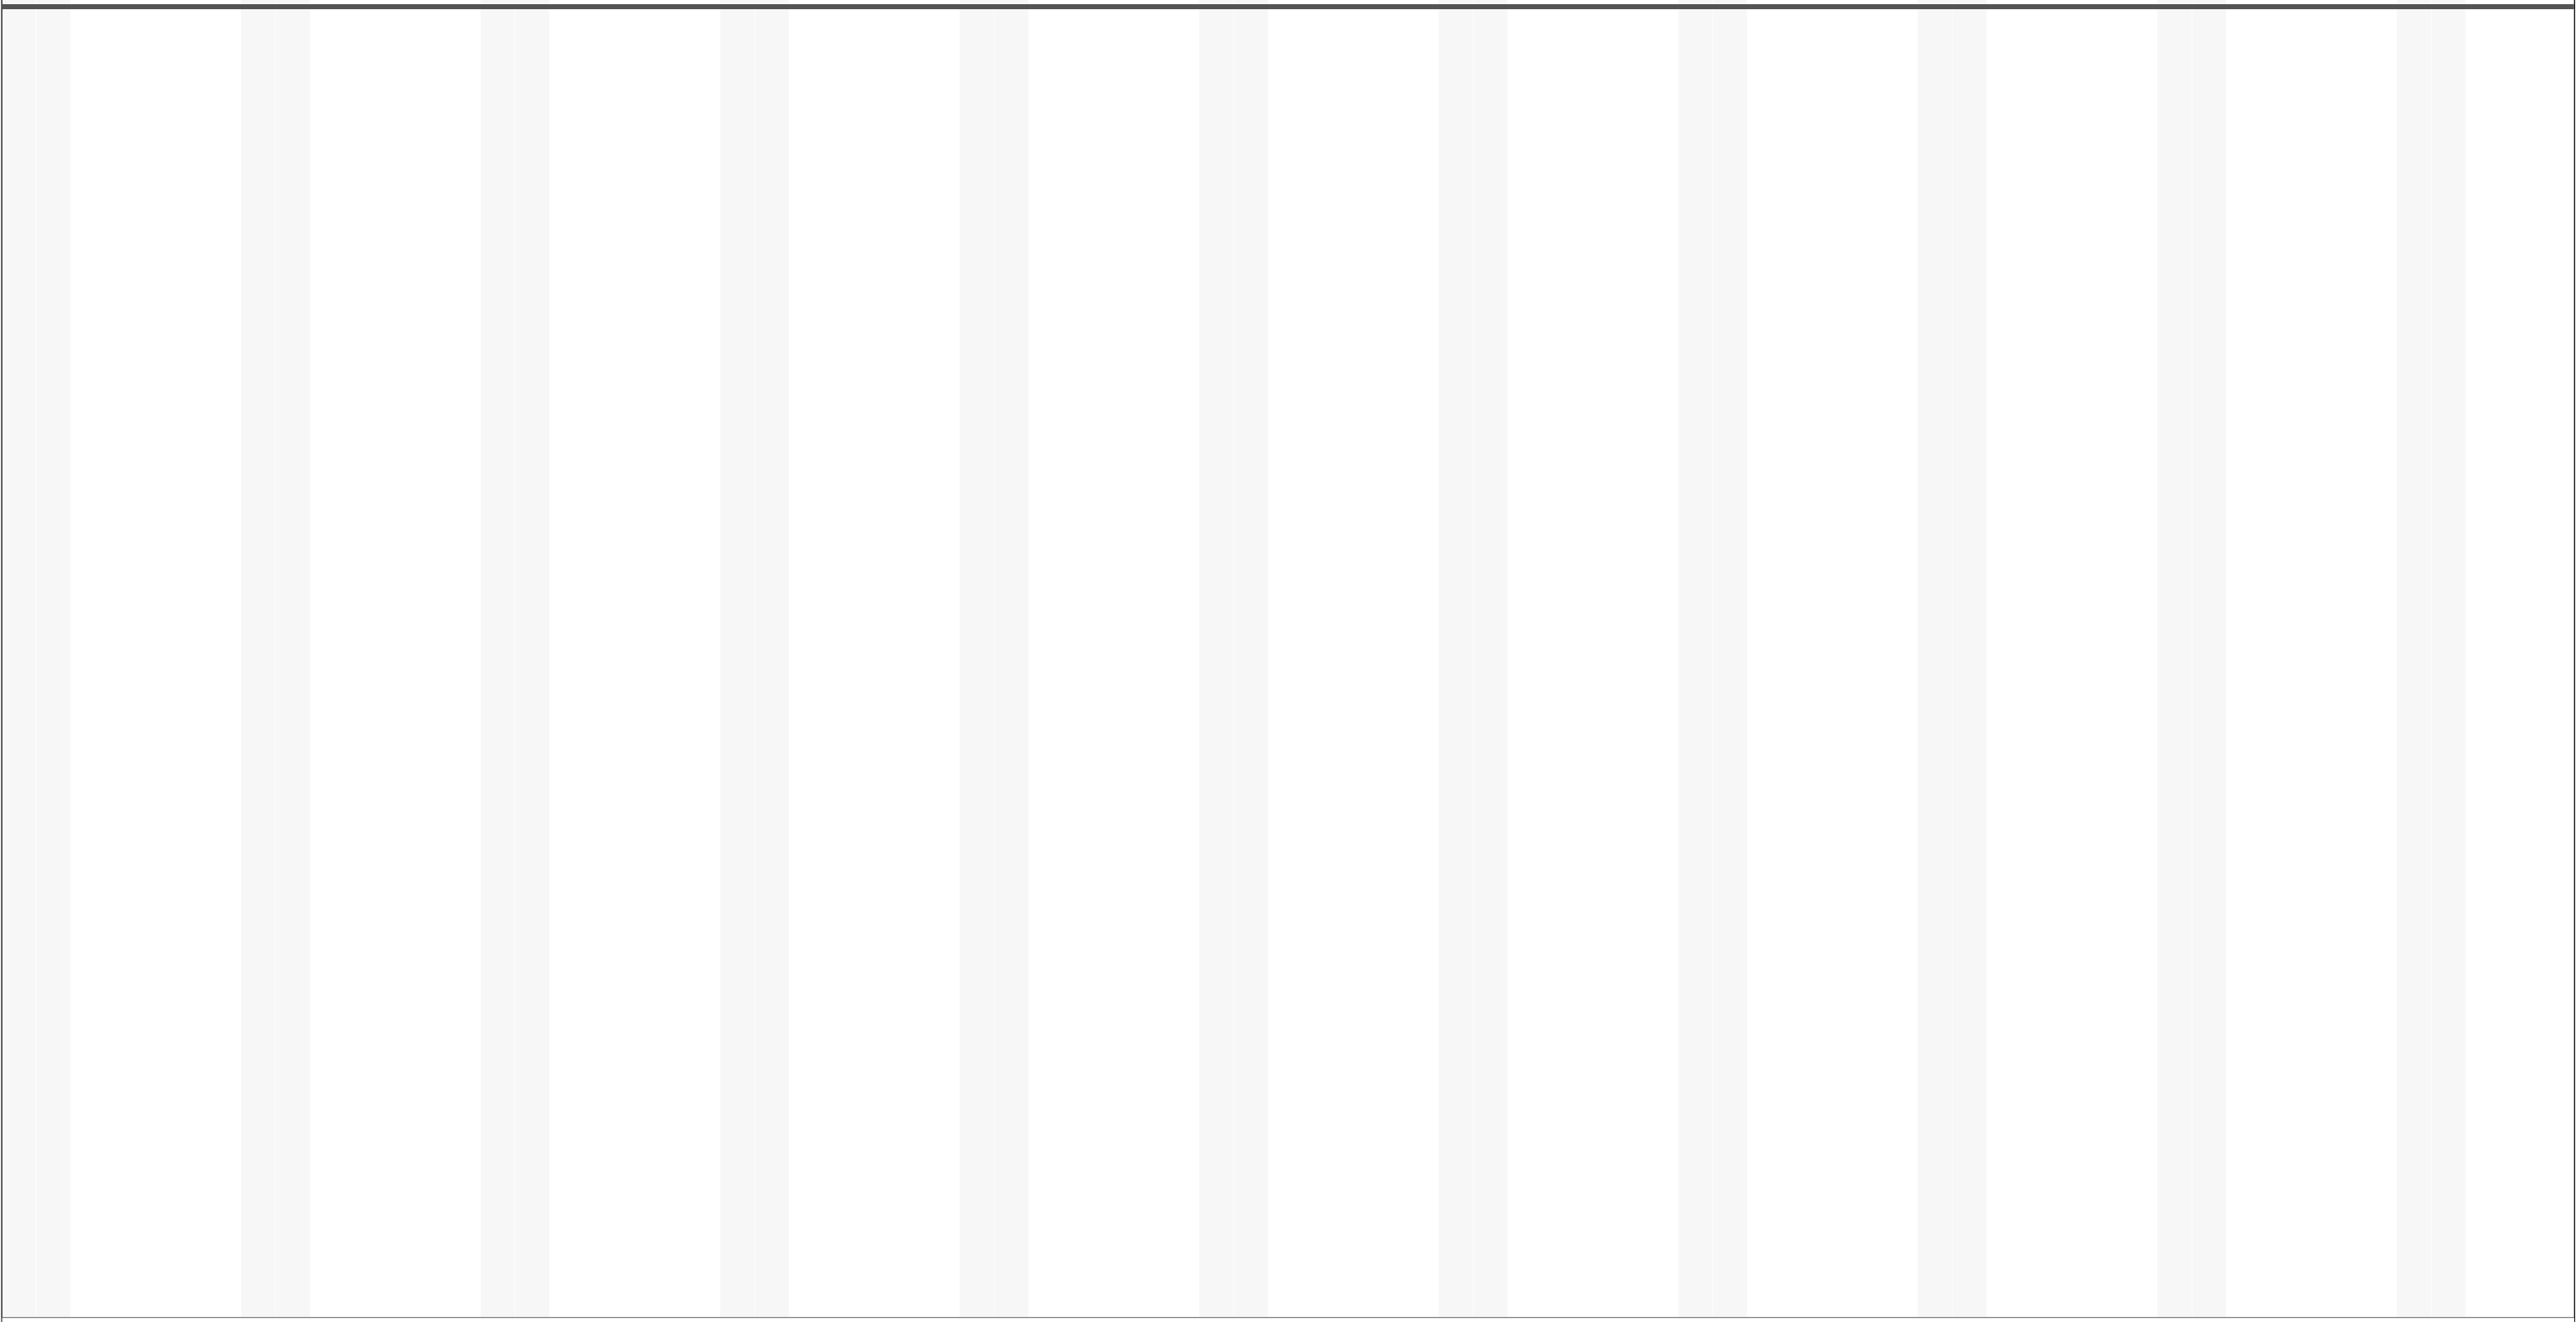


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S

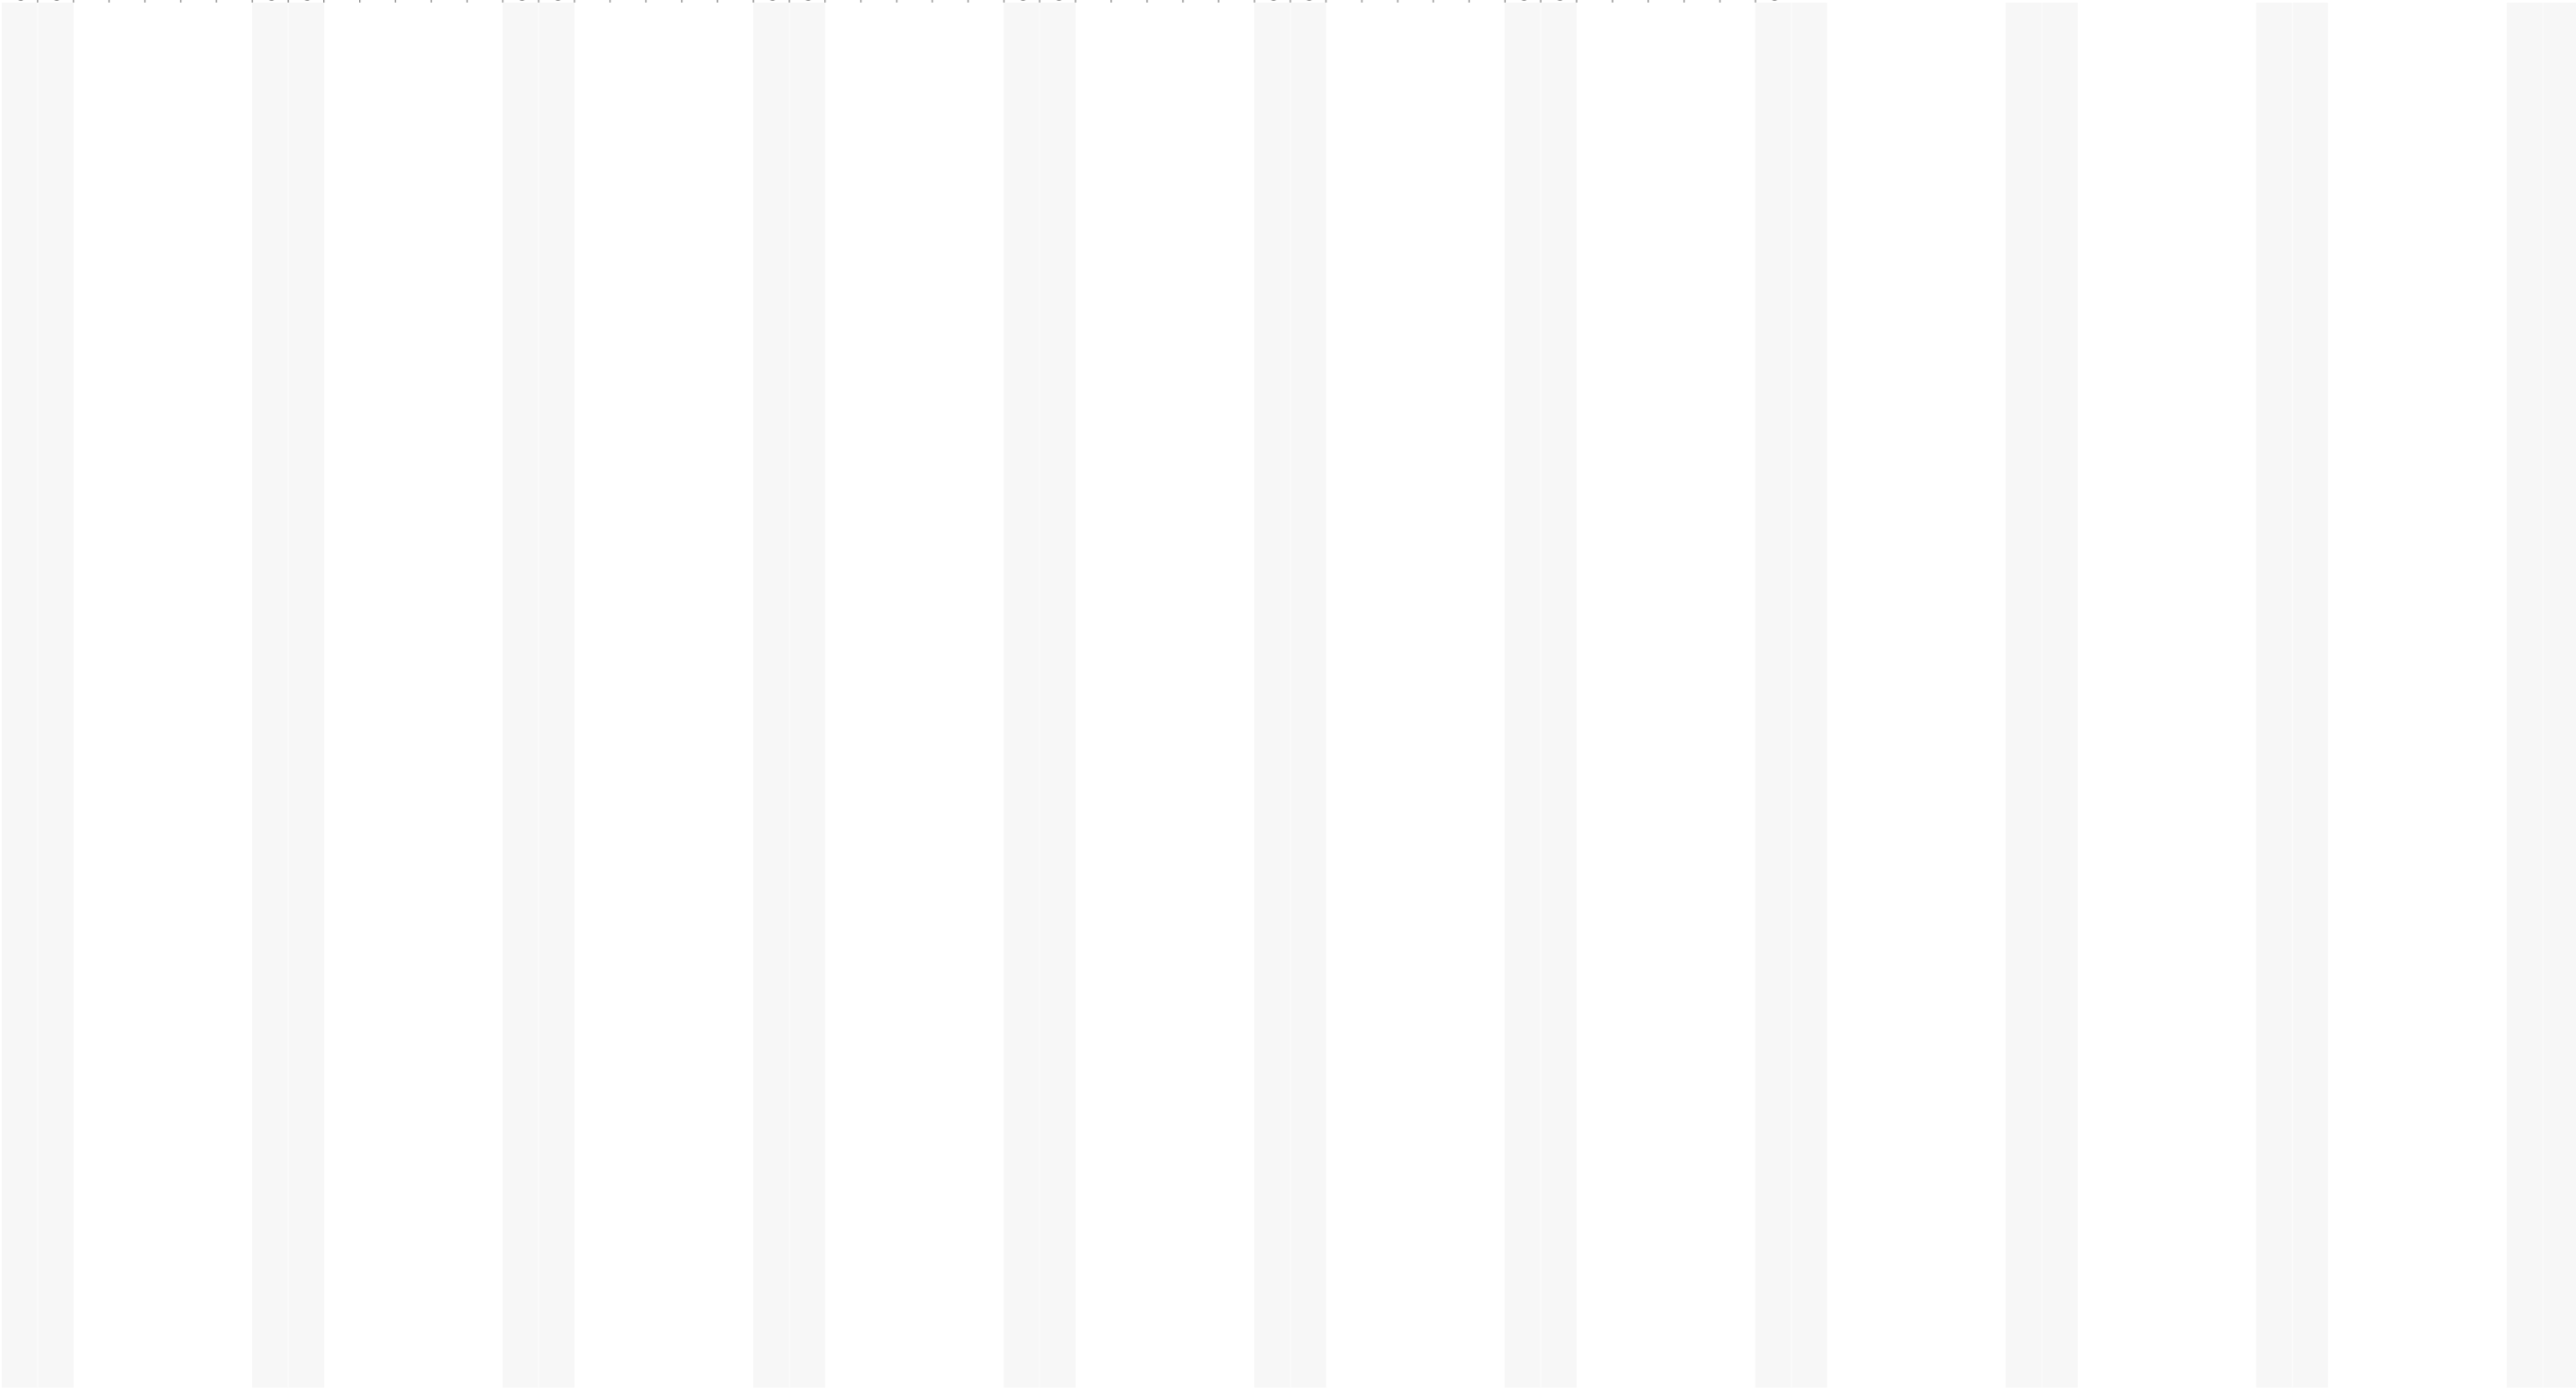




T F S S M

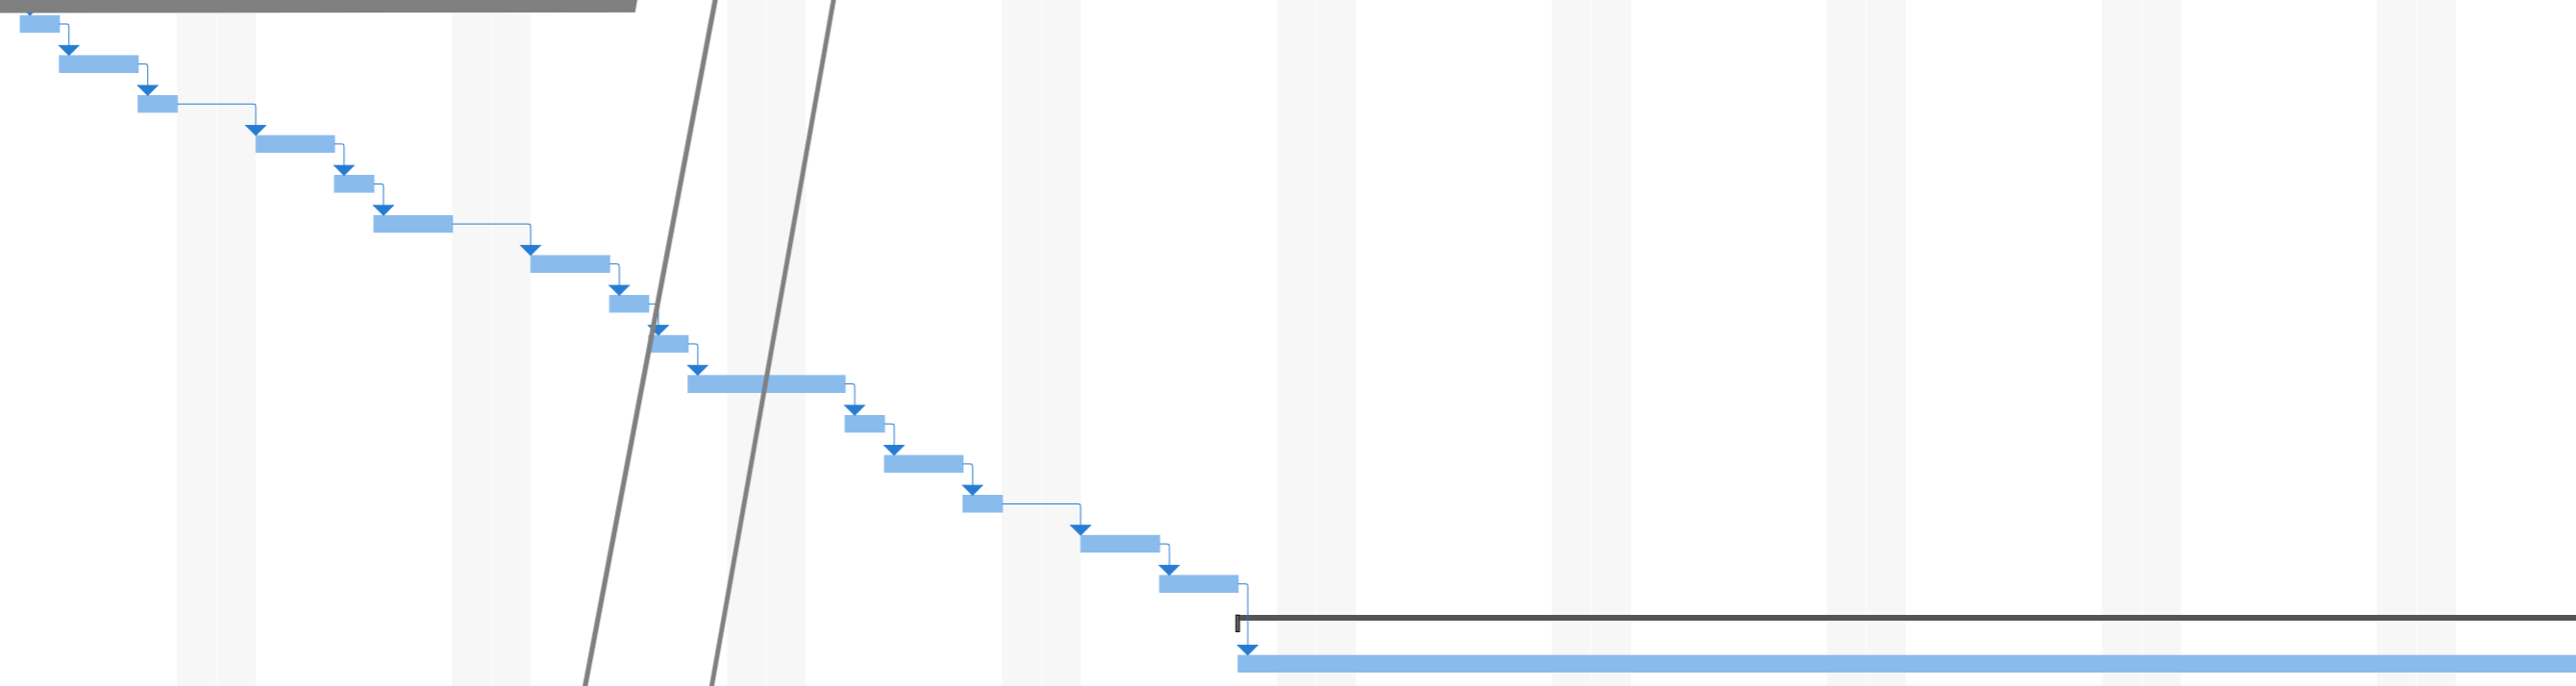

S | S | M | T | W | T | F | S | S | M | T | W | T | F |

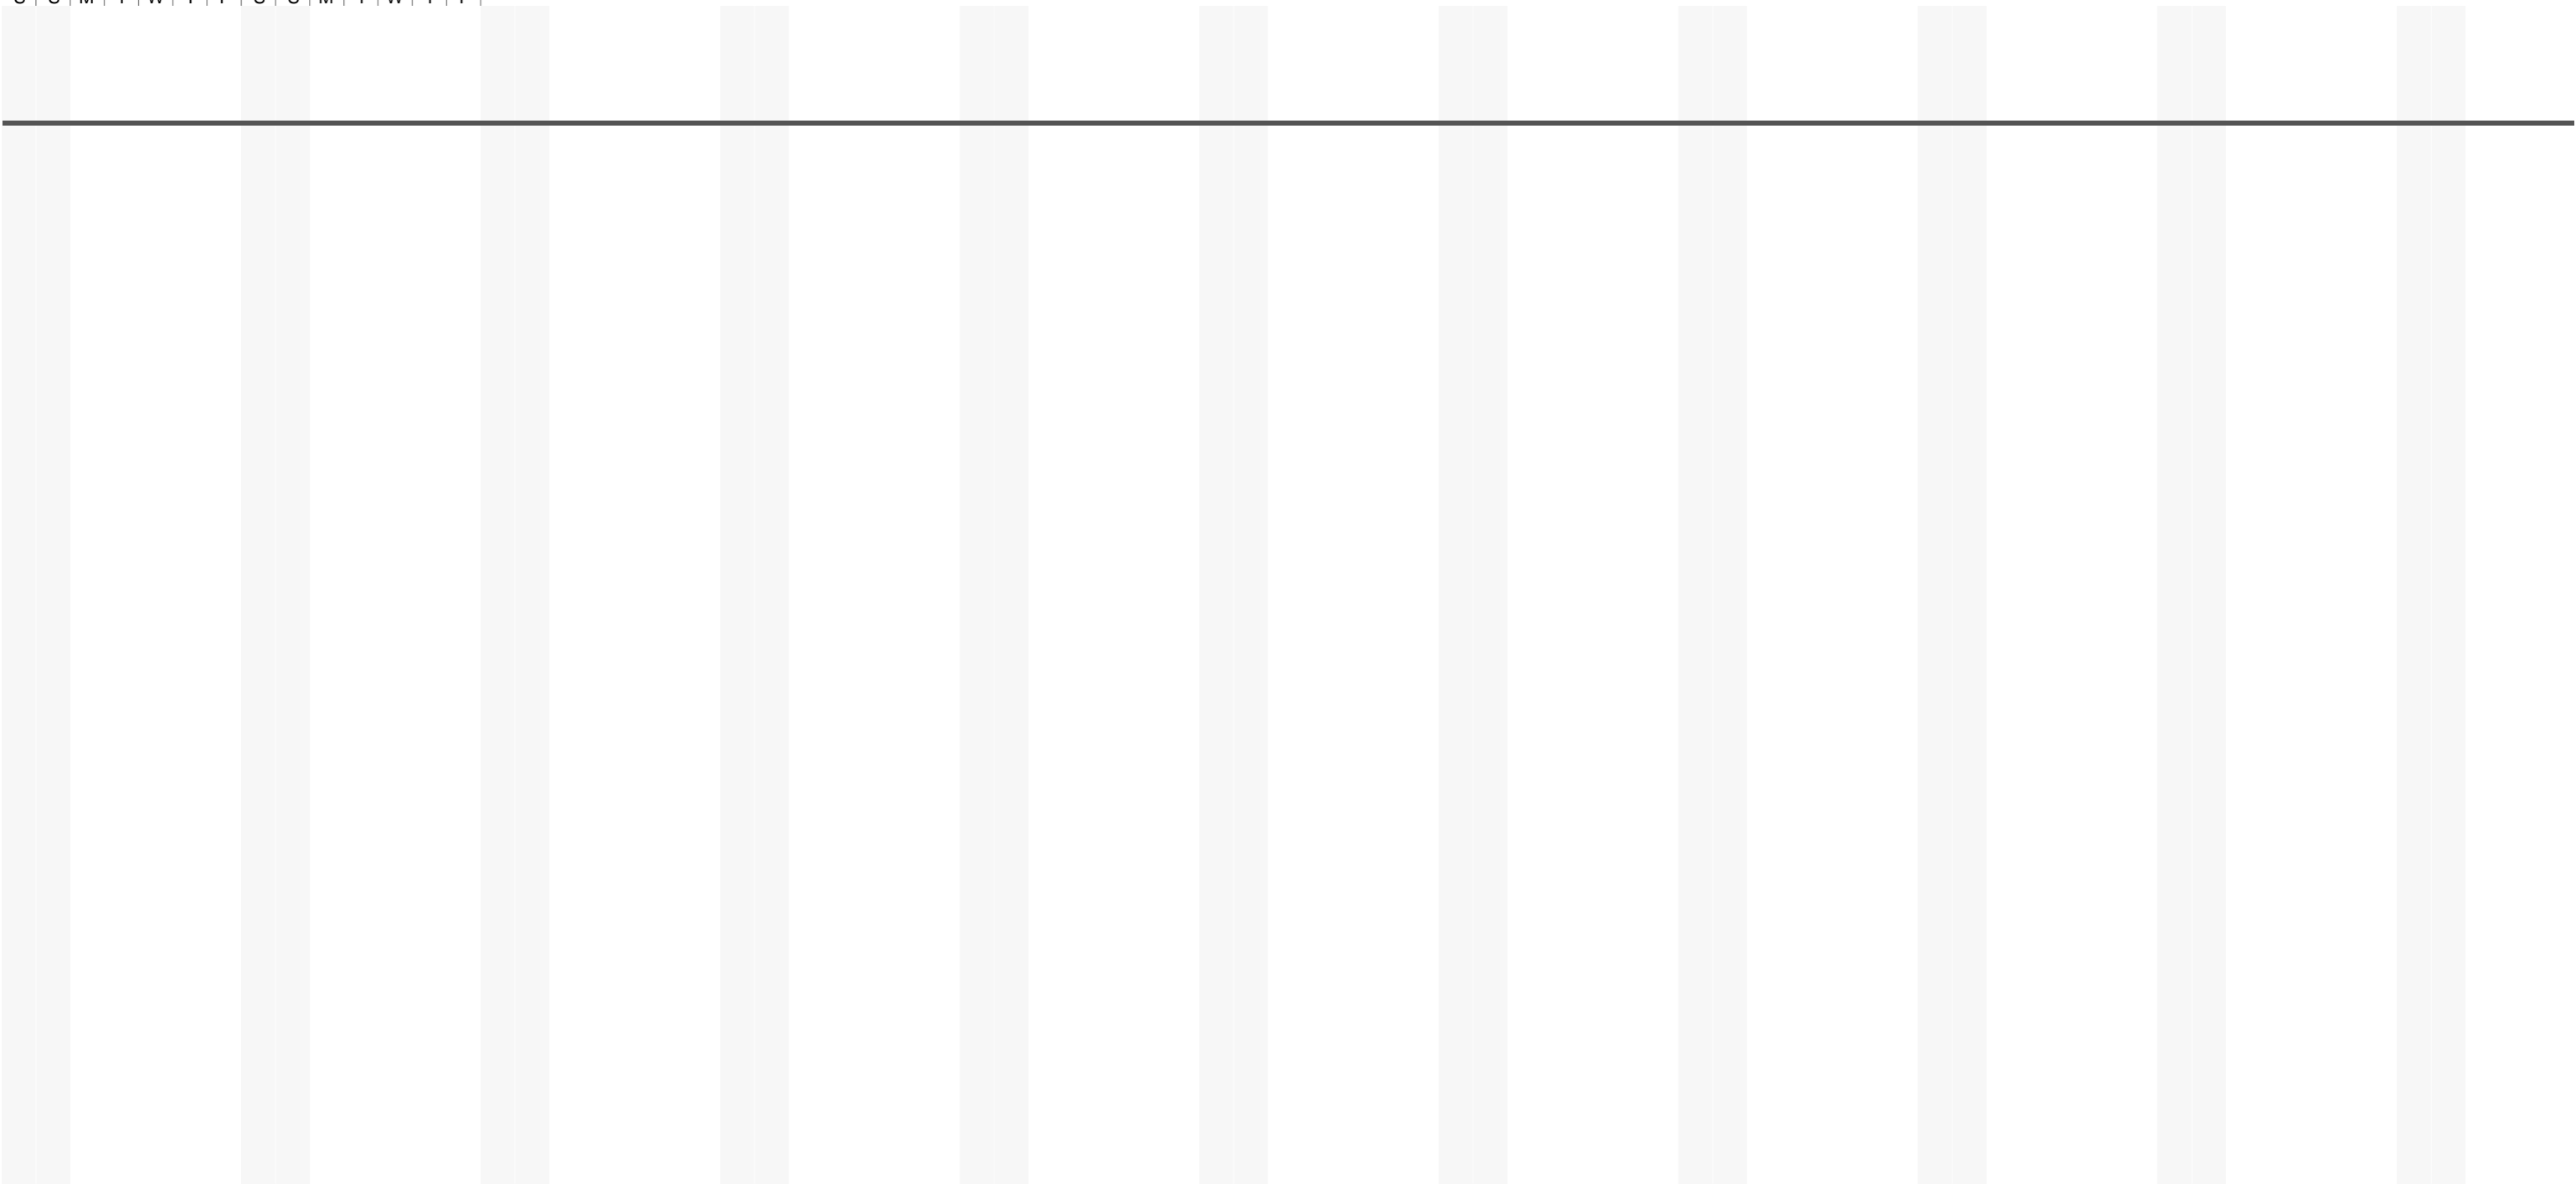




Task
Split






Task
Split




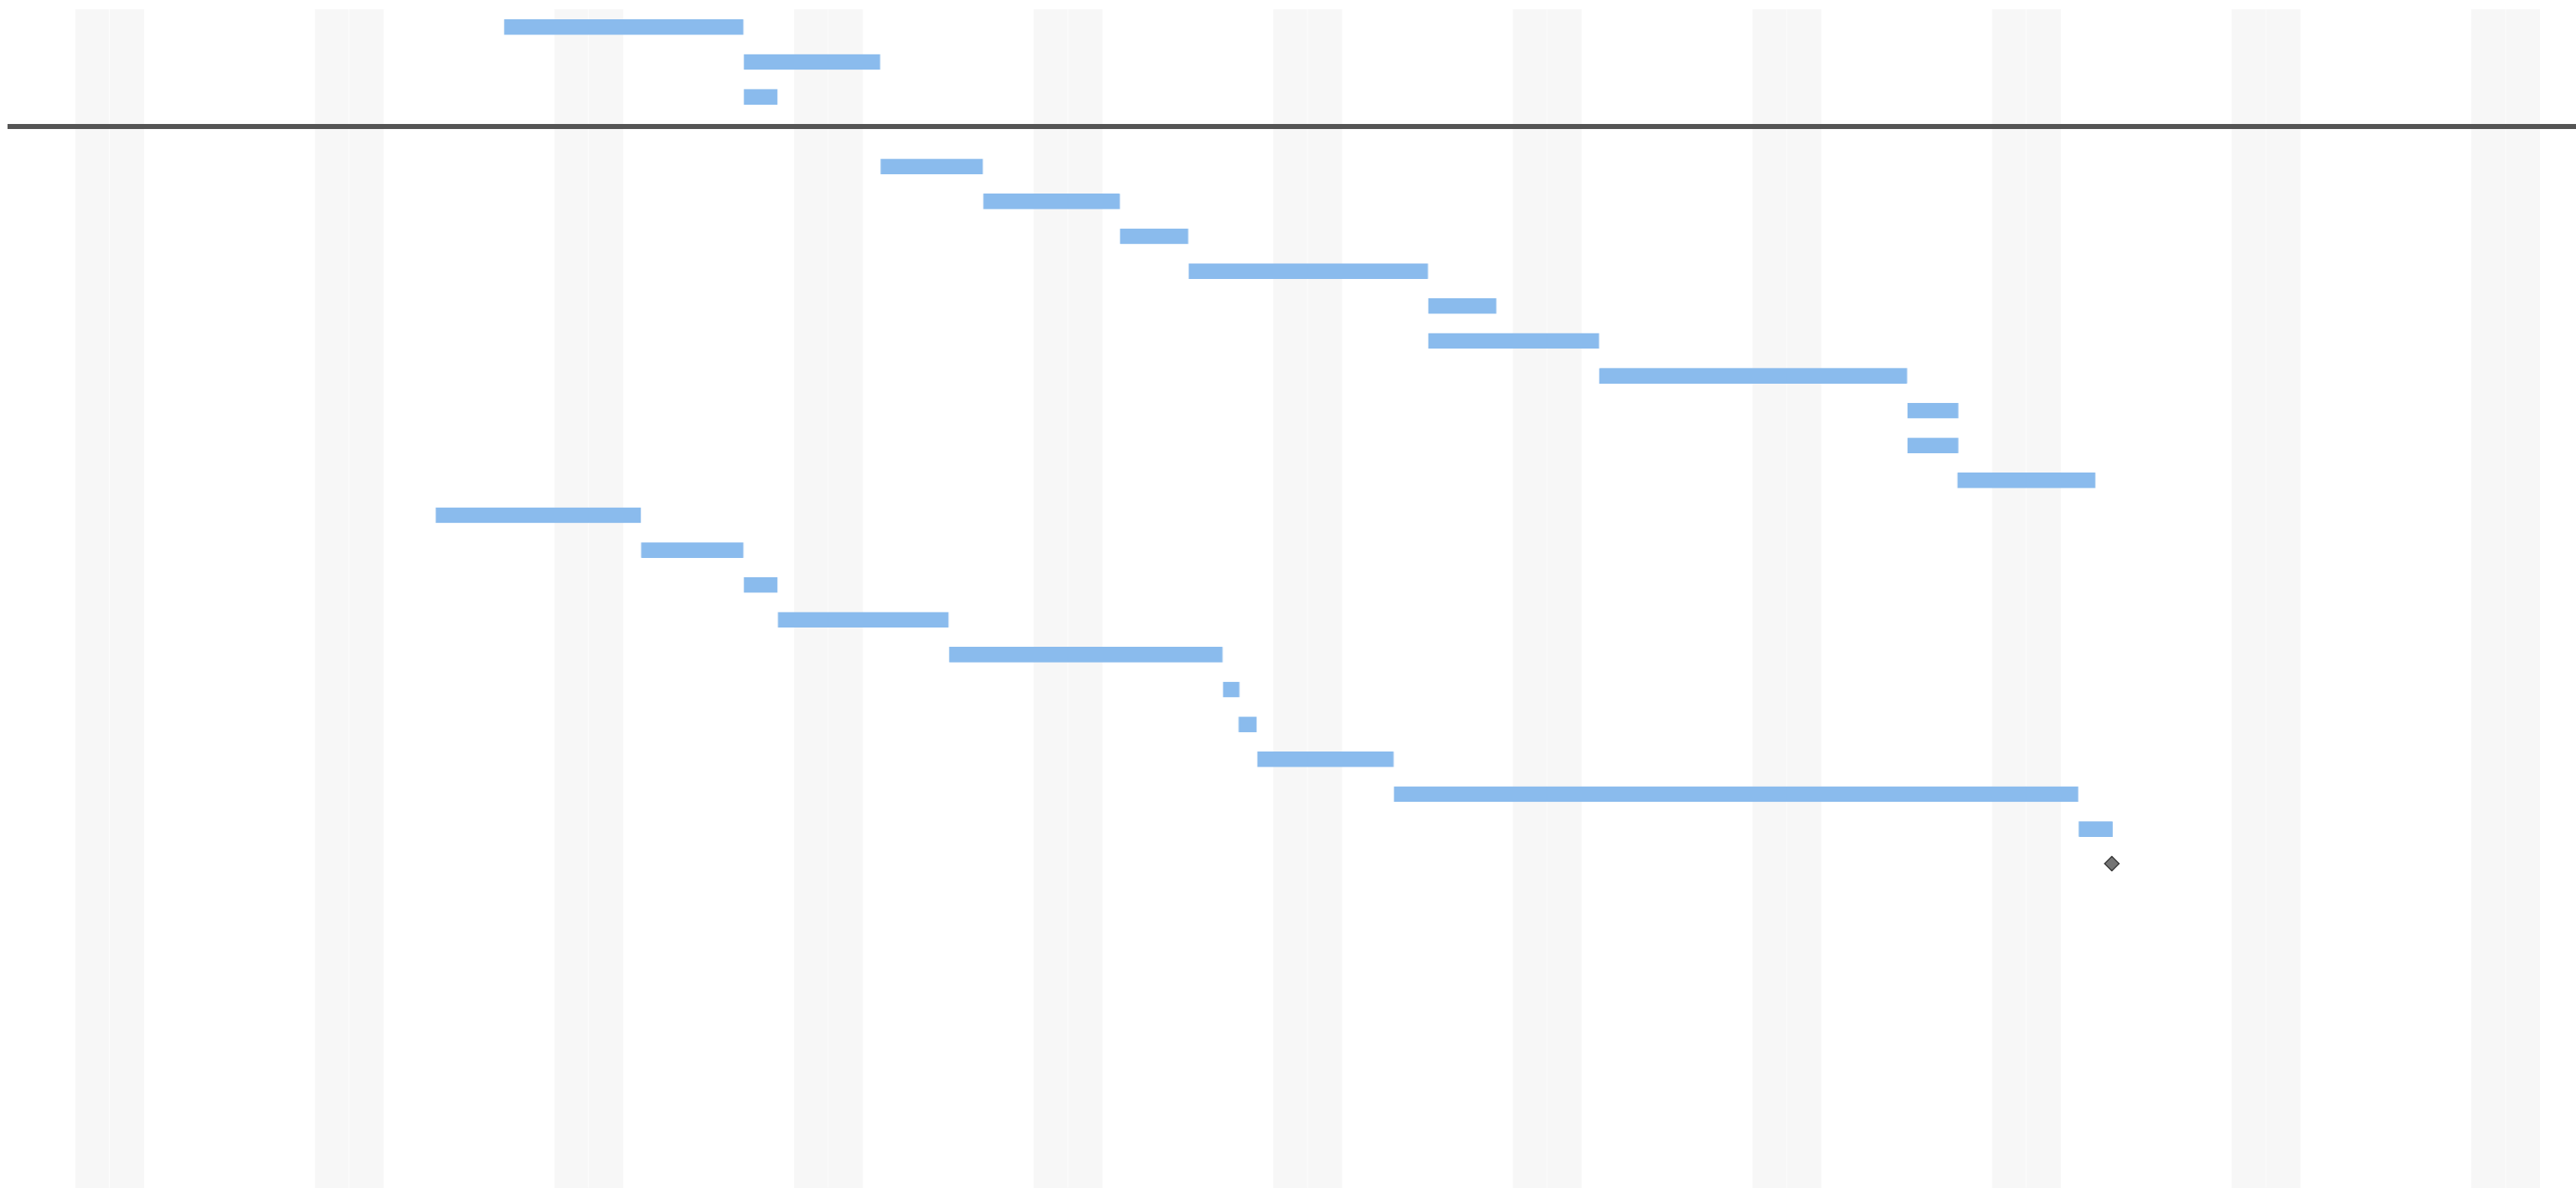


'22 Apr 17, '22 Apr 24, '22 May 1, '22 May 8, '22 May 15, '22 May 22, '22 May 29, '22 Jun 5, '22 Jun 12, '22 Jun 19, '22
 T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S

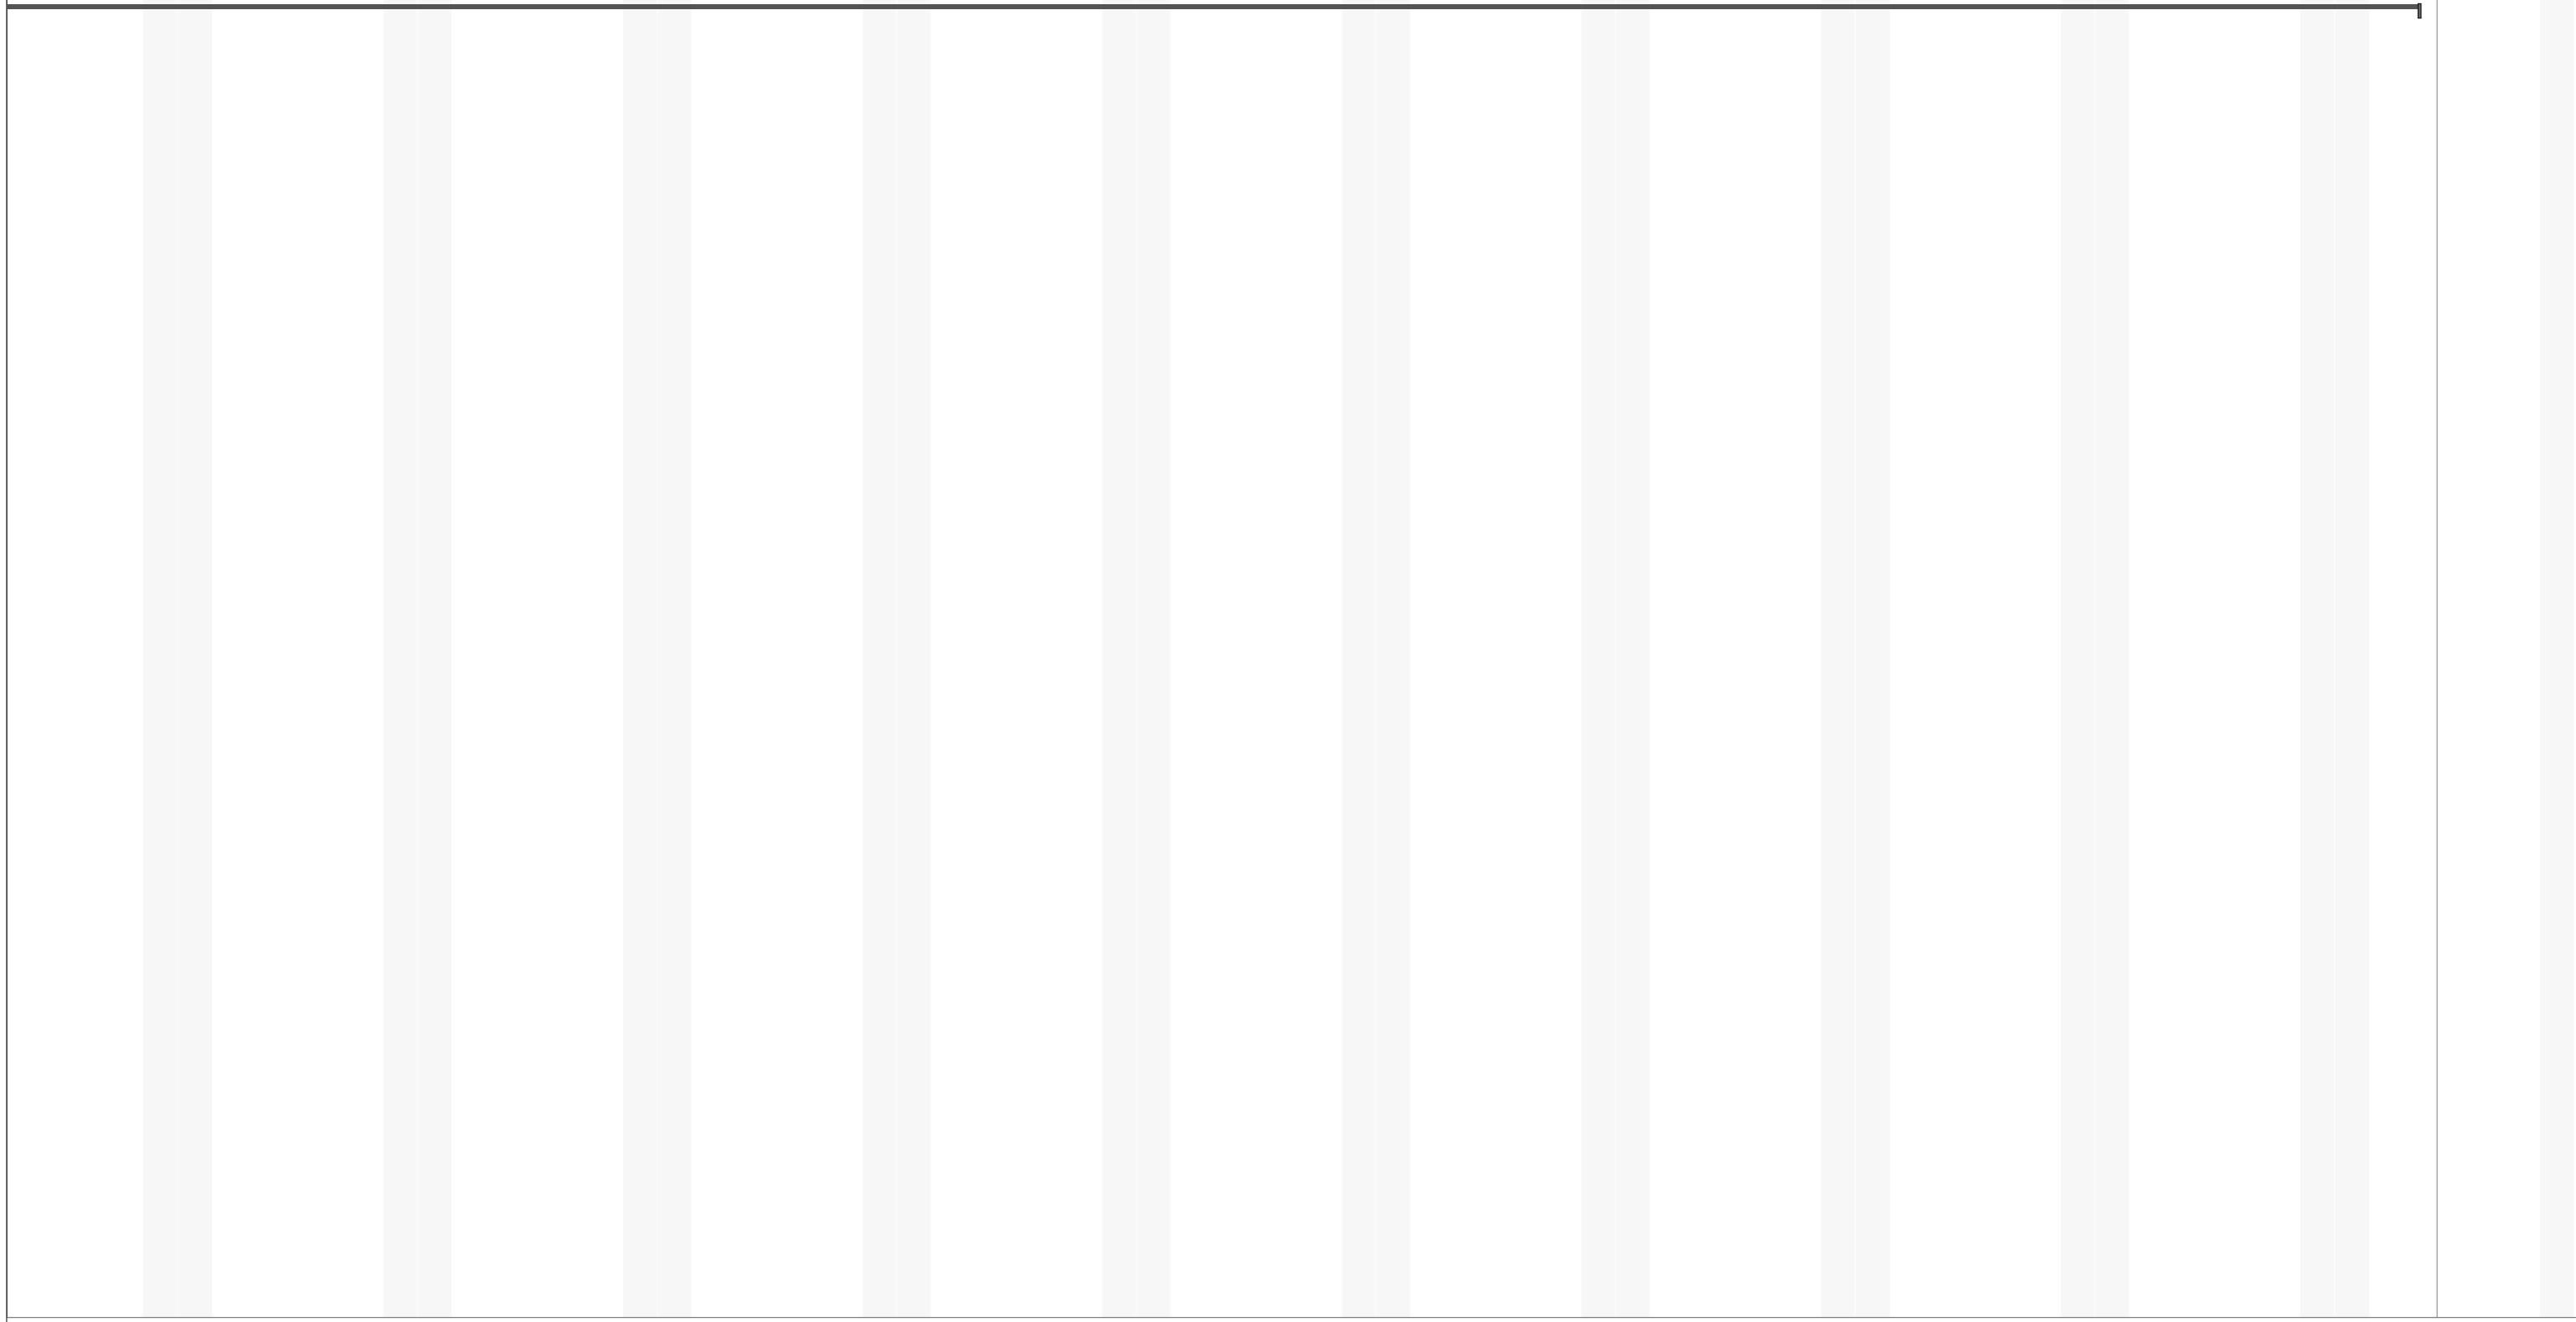

Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

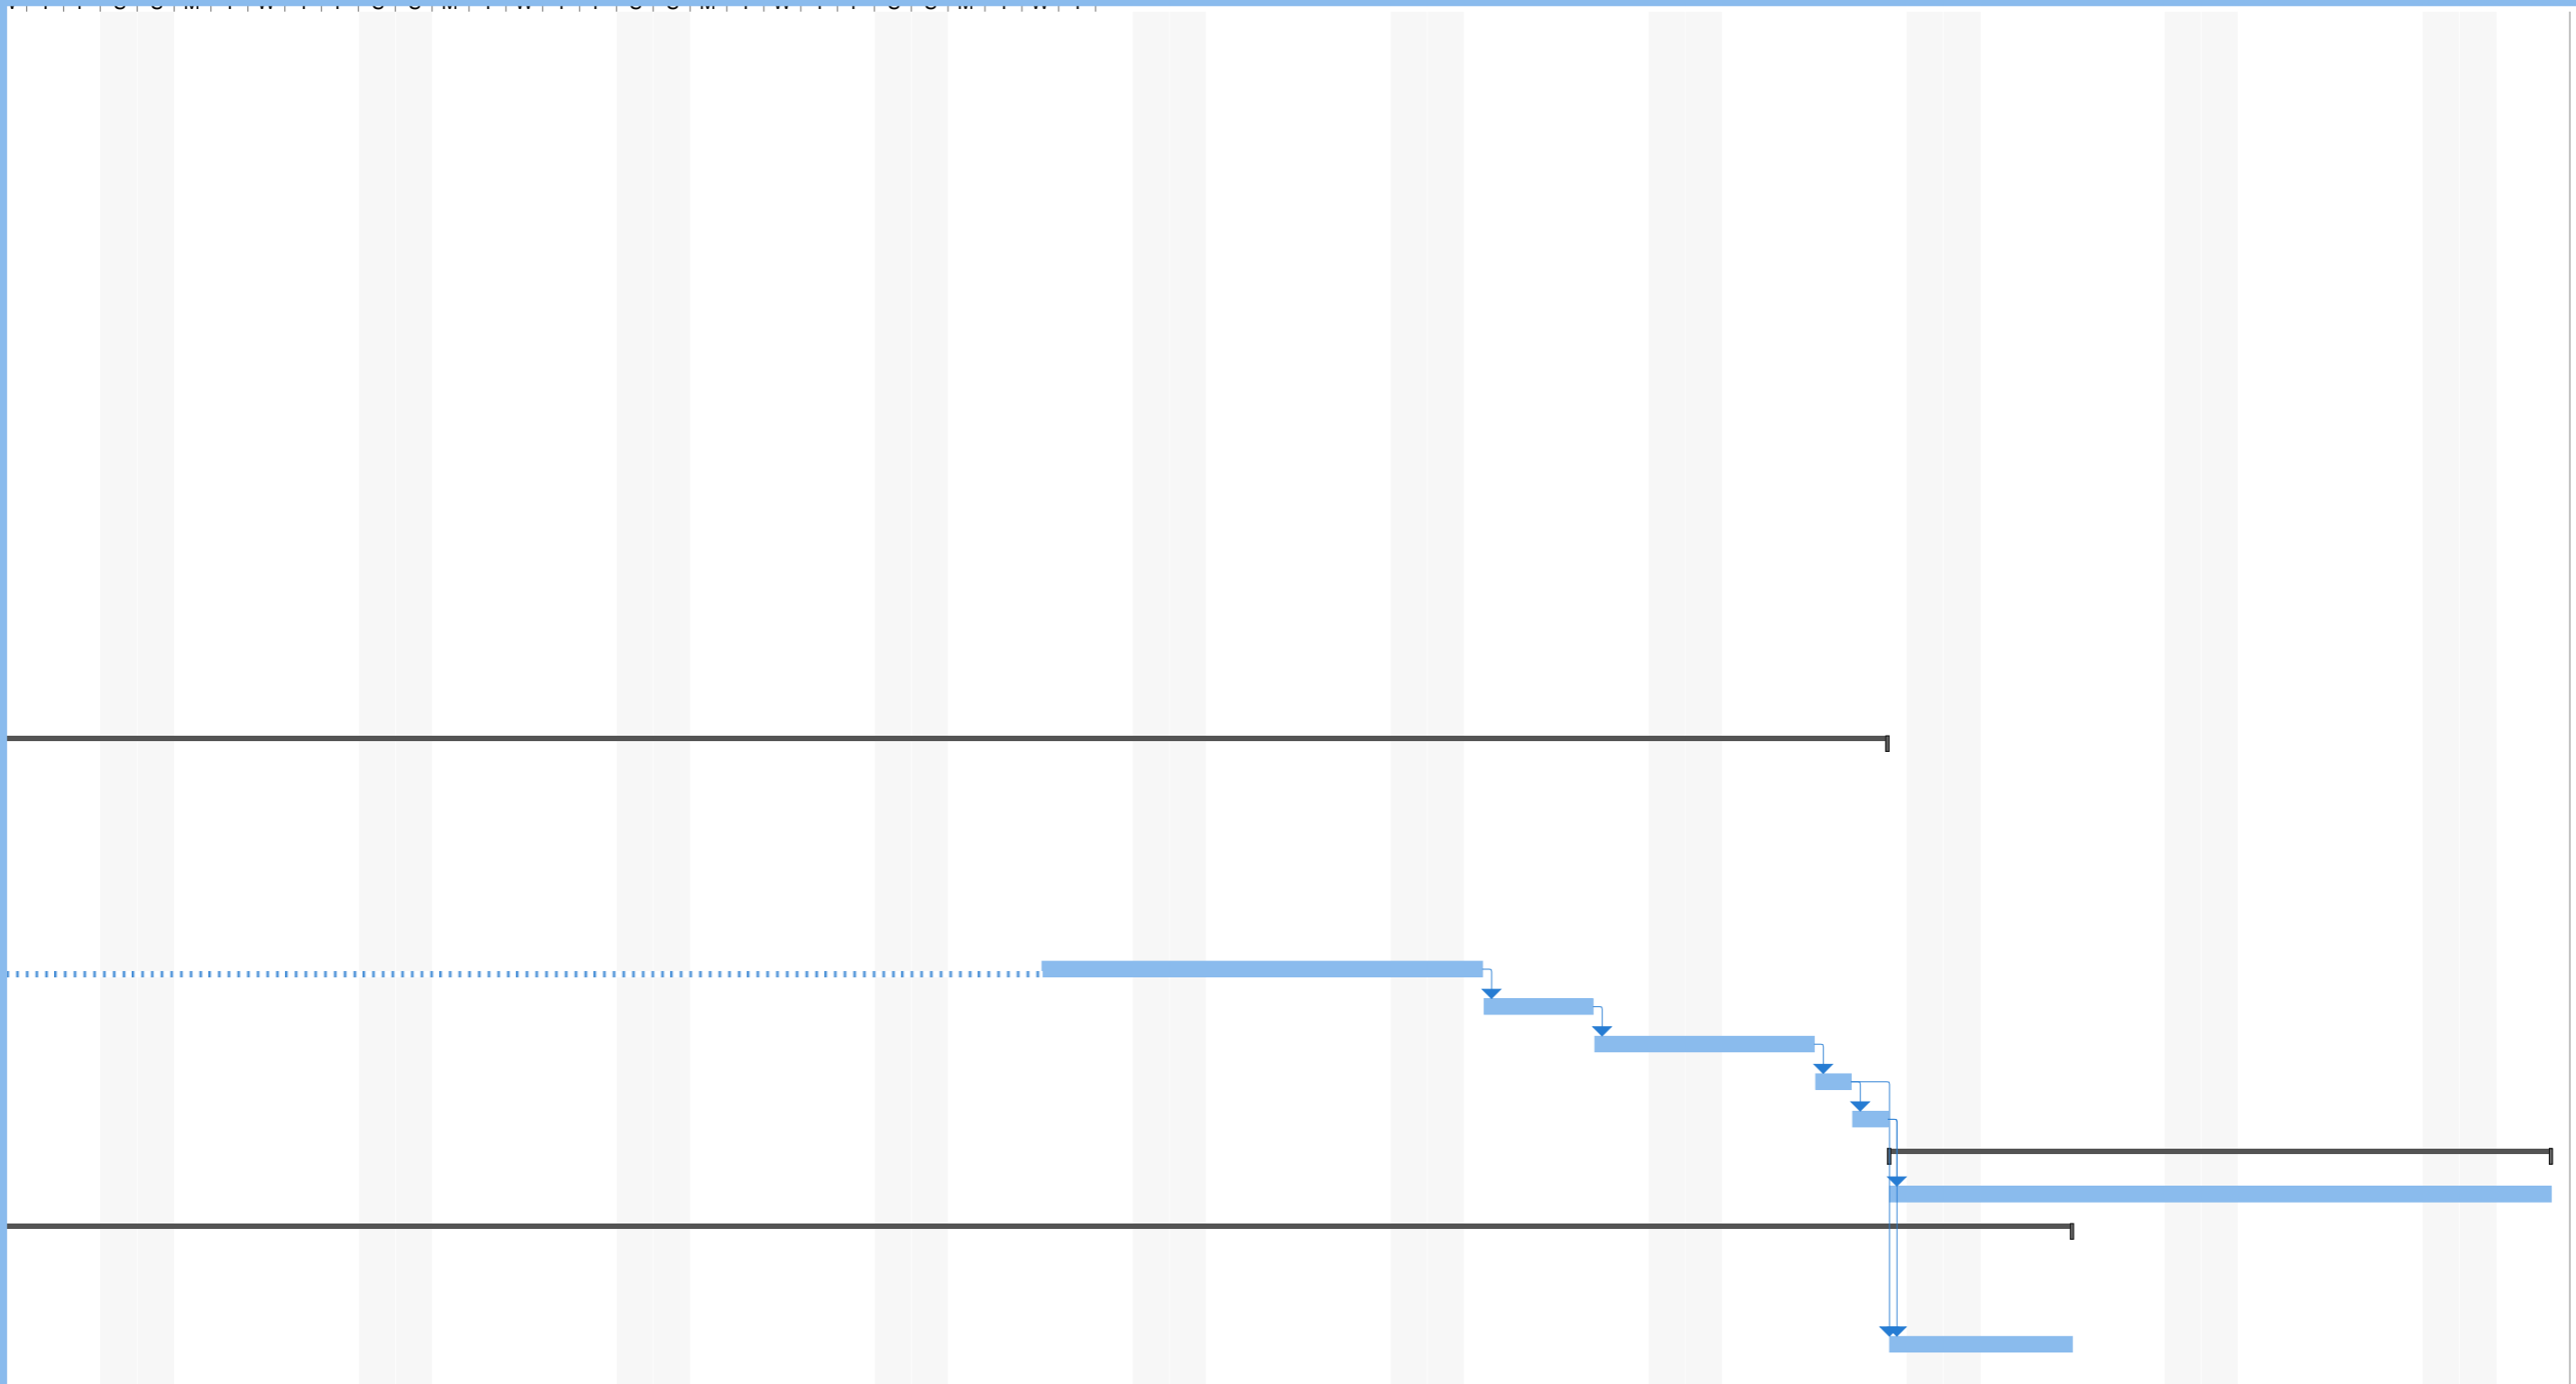


'22 Apr 17, '22 Apr 24, '22 May 1, '22 May 8, '22 May 15, '22 May 22, '22 May 29, '22 Jun 5, '22 Jun 12, '22 Jun 19, '22
T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S



Splt

Milestone

Sur



Description	Total days
Pre-Construction	155
Site-Work	82.25
Foundation	51
Retail System	40
Structural	90
Elevator/Stairs	34
Cladding	32.5
Mechanical/Electrical/Plumbing	48
Exterior Improvments	10
Finishes	113.5

